



Medicaid Management Information System Replacement (MMISR) Project

Working Draft

Release Strategy Plan

HSD Deliverable Owner: Paul Price

System Integrator (SI) Deliverable Owner: Adrian Ball

Configuration Number v0.5

November 26, 2018



Section 508
Compliant



Confidentiality Notice: This document, including any attachments, is for the sole use of the intended recipients and may contain confidential and privileged information, which must be protected from public disclosure. Any unauthorized review, use, disclosure, or distribution is prohibited. If you are not the intended recipient, please contact the sender and destroy all copies of the original document.

Table of Contents

1	Introduction	1
1.1	Overview.....	1
1.2	Purpose.....	1
1.3	Relationship with Other MMISR Project Plans.....	1
1.4	Plan Maintenance and Update.....	3
2	Overall Release Strategy	4
2.1	Release Types and Naming Conventions.....	5
2.1.1	Release Types	6
2.2	Release Naming Convention	7
2.2.1	MMISR Module Release Naming Convention	8
2.2.2	MMISR System Release Naming Convention.....	9
2.3	Planning Phase	9
2.3.1	Prepare for Release CCB.....	10
2.3.2	Conduct Release CCB	12
2.3.3	Prepare RBP.....	15
2.3.4	Conduct RBR.....	17
2.3.5	Planning Phase Exceptions.....	19
2.4	Implementation Phase	19
2.4.1	Conduct Implementation Readiness Review	20
2.4.2	Build-and-Deploy Implementation Test Environments	22
2.4.3	Conduct Implementation Testing.....	26
2.4.4	Build-and-Deploy Training Environment.....	28
2.4.5	Conduct End-User Training	28
2.4.6	Conduct O&M Team Training.....	30
2.4.7	Conduct Operational Readiness Review	32
2.5	O&M Phase.....	34
2.5.1	Build-and-Deploy Production Environments	35
2.5.2	Conduct Operational Testing	36
2.5.3	Conduct Production Readiness Review.....	37

2.5.4	Operate and Maintain in Production	38
2.5.5	Conduct Post Implementation Review.....	41
2.6	Module Contractor Release Strategy Oversight.....	43
2.6.1	Planning Phase Oversight.....	43
2.6.2	Implementation Phase Oversight.....	43
2.6.3	O&M Phase Oversight	43
2.7	Release Scope.....	44
2.8	Release Schedule.....	56
2.9	Release Notifications.....	57
2.9.1	Release Pre-Go-Live Notifications.....	58
2.9.2	Release Go-Live Notifications.....	58
2.9.3	Actors	59
2.10	Release Strategy Process Improvement.....	59
2.11	Release Strategy Training	60
3	Medicaid Management Information System Certification.....	61
4	Applicable Standards	61
5	Assumptions/Constraints/Risks.....	61
5.1	Assumptions	61
5.2	Constraints	61
5.3	Risks.....	61
6	Requirements Traceability	62
7	Appendices.....	62
7.1	Appendix A: List of Acronyms.....	62
7.2	Appendix B: Glossary.....	65
7.3	Appendix C: MECT Checklist.....	65
7.4	Appendix D: RBP Template.....	65
7.5	Appendix E: Sample NM HSD Release Notes	65
7.6	Appendix F: Record of Changes.....	68
8	Deliverable Format	70

9	Deliverable Acceptance Criteria.....	70
10	Deliverable Schedule.....	70

DRAFT

List of Figures

Figure 1: Release Strategy Phases.....	5
Figure 2: MMISR Project Environments.....	5
Figure 3: MMISR Modules.....	8
Figure 4: Planning Phase	10
Figure 5: Implementation Phase.....	19
Figure 6: Build-and-Deploy Process Life Cycle	24
Figure 7: Continuous Integration	25
Figure 8: Continuous Deployment	26
Figure 9: Implementation Testing.....	27
Figure 10: O&M Phase	34
Figure 11: Operational Testing.....	37
Figure 12: Operational Testing.....	66

List of Tables

Table 1: RSP Relationship to Other Project Plans.....	1
Table 2: MMISR Module Releases	4
Table 3: PCR Categories	11
Table 4: Prepare-for-Release CCB Process Actors	11
Table 5: Conduct Release CCB Process Description.....	13
Table 6: Actors Involved in Conduct CCB Meeting Process	14
Table 7: Prepare RBP Process Actors	17
Table 8: Conduct RBR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs.....	17
Table 9: Conduct RBR Process Actors	18
Table 10: IRR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs	21
Table 11: Conduct IRR Process Actors	22

Table 12: Build/Deploy Types	22
Table 13: Build/Deploy Tools	23
Table 14: Build-and-Deploy Implementation Test Environments Process Actors	24
Table 15: Conduct Implementation Testing Process Actors	28
Table 16: Conduct End-User Training Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs.....	28
Table 17: Conduct End-User Training Process Actors.....	30
Table 18: Conduct O&M Training Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs	30
Table 19: Conduct O&M Training Process Actors	31
Table 20: ORR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs.....	33
Table 21: Conduct Operational Readiness Review Process Actors.....	34
Table 21: Sample MMISR Production Outage Notification.....	35
Table 23: Actors of Operational Testing	37
Table 24: PRR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs	37
Table 25: Conduct Production Readiness Review Actors	38
Table 26: Operate and Maintain in Production Process Actors.....	40
Table 27: PIR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs	41
Table 28: Conduct Post Implementation Review Process Actors	42
Table 29: MMISR R1.0.0 Module Release Scope	45
Table 30: MMISR R1.0.0 Module Release Dates ¹	56
Table 31: Sample MMISR Release Pre-Go-Live Notification	58
Table 32: Sample MMISR Release Go-Live Notification.....	59
Table 33: Release Notification Process Actors.....	59
Table 34: List of Acronyms	62
Table 35: Record of Changes	68
Table 36: Deliverable Acceptance Criteria.....	70
Table 37: Deliverable Schedule	70

1 Introduction

1.1 Overview

The New Mexico (NM) Human Services Department (HSD) has adopted the Health and Human Services (HHS) 2020 vision, a transformational, enterprise approach to the health and human services business. HHS 2020 will move service delivery from a program-centric approach to a stakeholder-centric approach. NM HSD will migrate away from program and technology silos into an integrated, flexible framework that supports service delivery and stakeholder interaction across HHS programs and organizations. HHS 2020 is technology-enabled, but includes rethinking organizational design, redesigning and streamlining business processes, and reducing barriers between organizations within the HHS enterprise.

Please see “Section 1: Introduction” in the Project Management Plan for a detailed MMISR project overview.

1.2 Purpose

The purpose of the MMISR Release Strategy Plan (RSP) is to establish and manage the intricate MMISR release processes necessary to successfully move releases through the planning, implementation and operations and maintenance (O&M) phases of the Centers for Medicare and Medicaid Management Systems (CMS) eXpedited Life Cycle (XLC). No MMISR releases will go-live in the production environment until the initial big-bang MMISR production go-live in 2021. Releases will be promoted through the lower development and test environments prior to being promoted to the implementation environments. There, releases must successfully interoperate using test data until ultimately being promoted to the production environment as part of the initial big-bang MMISR production go-live in 2021. The RSP leverages CMS's XLC and best practices for implementing similarly complex large multi-project and multi-vendor programs. The intended audience of the RSP are the MMISR project business sponsors, the State-led Project Management Office (PMO), the System Integration (SI) Contractor, and module contractors.

1.3 Relationship with Other MMISR Project Plans

The RSP references other MMISR project plans. The following table identifies the referenced plans and describes their relationship to the RSP.

Table 1: RSP Relationship to Other Project Plans

Plan Name	Relationship to RSP
Change Control Management Plan (CCMP)	The CCMP defines the process used enterprise-wide by the SI Contractor, module contractors, and the State-led PMO to ensure all MMISR project changes are captured, communicated, and understood. If project stakeholders must go outside of the project parameters, which are the triple constraints, then the CCMP ensures there is a review, agreement, and communication prior to

Plan Name	Relationship to RSP
	versus after the fact. The RSP provides an overview of the CCMP processes and artifacts used during the planning phase.
Configuration Management Plan	The Configuration Management Plan defines the process used enterprise-wide by the SI Contractor, module contractors, and the State-led PMO to identify, name, and track the MMISR project individual hardware, software, and documentation configuration items (CIs) to ensure MMISR project and system integrity. The RSP provides an overview of Configuration Management Plan processes and artifacts used for naming MMISR releases and managing MMISR module CIs.
Communications Management Plan	The Communications Management Plan defines the process used enterprise-wide by the SI Contractor, module contractors, and the State-led PMO to ensure the information needs of the MMISR project are met by developing the artifacts and executing the activities designed to achieve effective information exchange. The RSP provides an overview of the Communications Management Plan processes and artifacts used to notify stakeholders of the deployment of a MMISR release to the production environment.
Quality Management Plan (QMP)	The QMP defines the process used enterprise-wide by the SI Contractor, module contractors, and the State-led PMO to define, execute, review, and evaluate project processes that enhance the project team's ability to produce high-quality work products and deliverables in a manner consistent with internally and externally imposed policies and standards. The RSP provides an overview of the QMP processes and artifacts used during the O&M phase.
Test Management Plan (TMP)	The TMP defines the process used enterprise-wide by the SI and module contractors for testing activities across the MMISR enterprise solution, according to the CMS testing framework. The RSP provides an overview of the TMP processes and artifacts used during the implementation and O&M phases.
Training Plan and Training Manual	The Training Plan provides best practices for employing repeatable training development processes. The Training Manual will include training materials such as user manuals, training aids, tip sheets, checklists, and other forms of documentation for the tools and technologies that are part of the SI platform. The RSP provides an overview of the Training Plan processes and Training Manual materials used during the implementation phase.
O&M Plan and O&M Manual	The O&M Plan describes the roles and responsibilities, staffing model, support level, and processes to support a MMISR release during the O&M phase. The O&M Manual describes MMISR release items such as startup, shutdown, maintenance, and troubleshooting procedures. The RSP provides an overview of the

Plan Name	Relationship to RSP
	O&M Plan and O&M Manual processes and artifacts used during the O&M phase.
Staffing Model and Resource Management Plan	The Staffing Model and Resource Management Plan describes how the SI and module contractors will provide the required expertise over the project life, how a sufficient number of skilled staff members will be deployed on the project, and how the project team will be structured to effectively deliver the required work. The RSP provides an overview of the Staffing Model and Resource Management Plan processes for providing RSP training.

1.4 Plan Maintenance and Update

The RSP content will be revisited when it reaches federal or State phase-gate approval, when new module contractors are on-boarded, or at a minimum, annually by the SI Contractor. The SI Contractor will facilitate RSP reviews to ensure it is current, satisfies the MMISR project needs, and is relevant to the effective management of MMISR releases. The review and approval of RSP changes will follow the change management process documented in the MMISR CCMP and will be recorded in Appendix F: Record of Changes.

2 Overall Release Strategy

The MMISR RSP describes the system development life cycle (SDLC) processes, artifacts, and reviews associated with the planning, implementation, and O&M phases of the CMS XLC necessary to ensure a MMISR release delivers the agreed-to scope on the agreed-to go-live date in the MMISR production environment. A MMISR release consists of multiple MMISR module releases listed in following table. The table also identifies the module's type and whether the module supports application program interfaces (APIs).

Table 2: MMISR Module Releases

MMISR Module Release	Module Type	API/Non-API Module
Enterprise Service Bus (ESB)/Integration Platform (IP)	ESB/IP	Non-API
Systems Migration Repository (SMR)	SMR	Non-API
Master Data Management (MDM)	Enterprise Shared Service (ESS)	API
Customer Communications Management (CCM)	ESS	API
Address Standardization Verification and Validation (ASVV)	ESS	API
Electronic Documentation Management (EDM)	ESS	API
Identity and Access Management (IdAM)	ESS	API
Omnicaid (OC)	Legacy Module (LMI)	API
Automated System Program and Eligibility Network (ASPEN)	LMI	API
Child Support Enforcement System (CSES)	LMI	API
Department of Health (DoH) Systems	New Module (NMI)	API
Data Services (DS)	NMI	API
Quality Assurance (QA)	NMI	API
Benefit Management Services (BMS)	NMI	API
Financial Services (FS)	NMI	API
Unified Portal (UP)	NMI	Non-API
Consolidated Customer Service Center (CSCC)	NMI	Non-API
Interfaces (INT)	INT	Non-API
Service Orchestration (SO)	SO	API

The CMS XLC planning, implementation, and O&M phases, highlighted in **blue** in the figure below, are within the scope of the RSP. The CMS XLC requirements analysis, design, development, and test phases are excluded from the MMISR RSP's scope.


Figure 1: Release Strategy Phases



The purpose of the planning phase is to determine the release's scope and schedule. The purpose of the implementation phase is to: 1) determine the release's readiness to be promoted from the test phase environments to the implementation phase environments, 2) conduct implementation testing, 3) train, and 4) determine the release's readiness to be promoted to the O&M phase environments. The purpose of the O&M phase is to conduct release operational testing and turn the production-ready release over to the O&M team and end users.

The figure below identifies the MMISR project's environments and shows the movement of releases between environments.

Figure 2: MMISR Project Environments

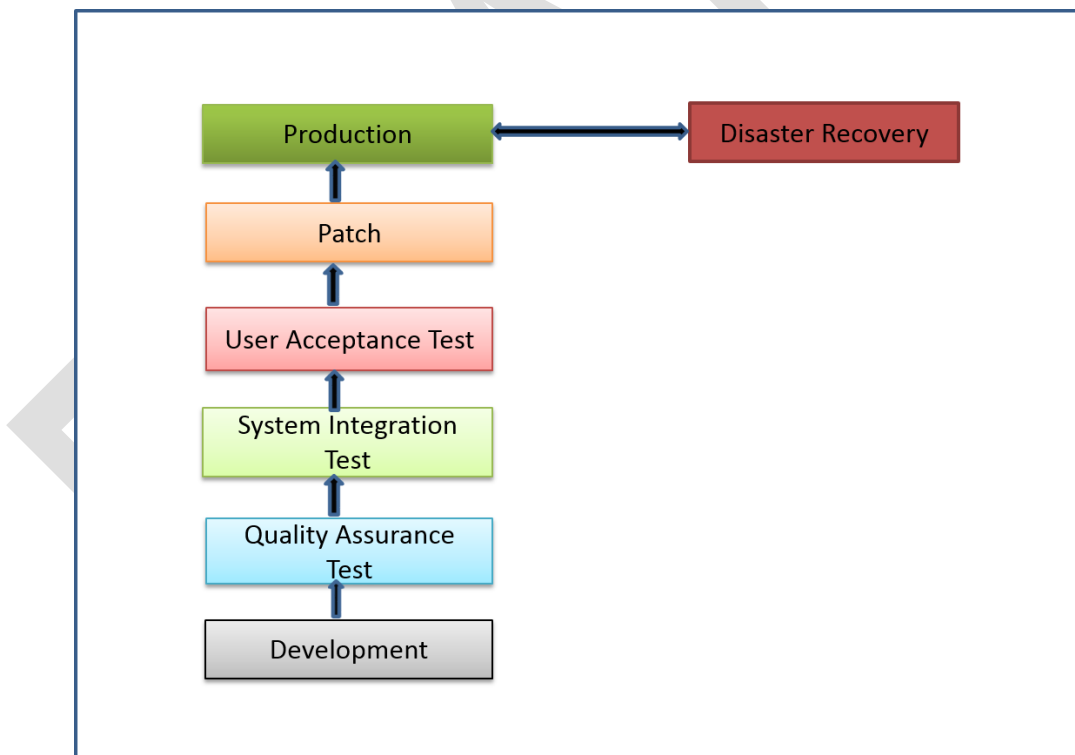

2.1 Release Types and Naming Conventions

Before describing the planning, implementation, and O&M phases in detail, it is important first to define the MMISR release types and release naming conventions.

2.1.1 Release Types

There are three release types:

- Major
- Minor
- Patch

Release type definitions exist for API and non-API modules.

2.1.1.1 Non-API Module Major Releases

Non-API module major releases deliver new features, for example:

- New SMR legacy data set
- New interface
- Major ESB/IP software upgrade

Non-API module major releases may also deliver minor and patch-level non-API module changes described in the following two subsections. These releases are deployed to the MMISR production environment on a recurring basis (for example, quarterly).

2.1.1.2 Non-API Module Minor Releases

Non-API module minor releases deliver feature enhancements and non-urgent fixes for known production defects, for example:

- Modified SMR legacy data set
- Modified interface
- Minor ESB/IP software upgrade

Non-API minor module releases may also deliver patch-level non-API module changes described in the following subsection and are deployed to the MMISR production environment on a recurring basis (for example, quarterly).

2.1.1.3 Non-API Module Patch Releases

Non-API module patch releases deliver urgent fixes for a small number of known production defects and are deployed to the MMISR production environment on an as-needed basis.

2.1.1.4 API Module Major Releases

API module major releases:

- Deliver backwards-incompatible changes
- May deliver minor- and patch-level API changes
- Are deployed to the MMISR production environment on a recurring basis (for example, quarterly)

2.1.1.5 API Module Minor Releases

API module minor releases:

- Deliver backwards-compatible changes
- May deliver patch-level API changes
- Are deployed to the MMISR production environment on a recurring basis (for example, quarterly)

2.1.1.6 API Module Patch Releases

API module patch releases:


- Deliver backwards-compatible defect fixes
- Are deployed to the MMISR production environment on an as-needed basis

2.2 Release Naming Convention

The MMISR Configuration Management Plan will provide a detailed description of the release naming convention. This section of the RSP provides an overview of that convention.

A release naming convention defines the rules for determining and assigning unique names to unique system releases. Release naming may appear trivial but is critical to the overall success of any effective release strategy. This section defines the release naming convention for major, minor, and patch releases.

Per Table 2 above and Figure 3 below, the MMISR system consists of several modules. Release names are determined and assigned to both MMISR modules and the MMISR system per the release naming conventions described in the following subsections.

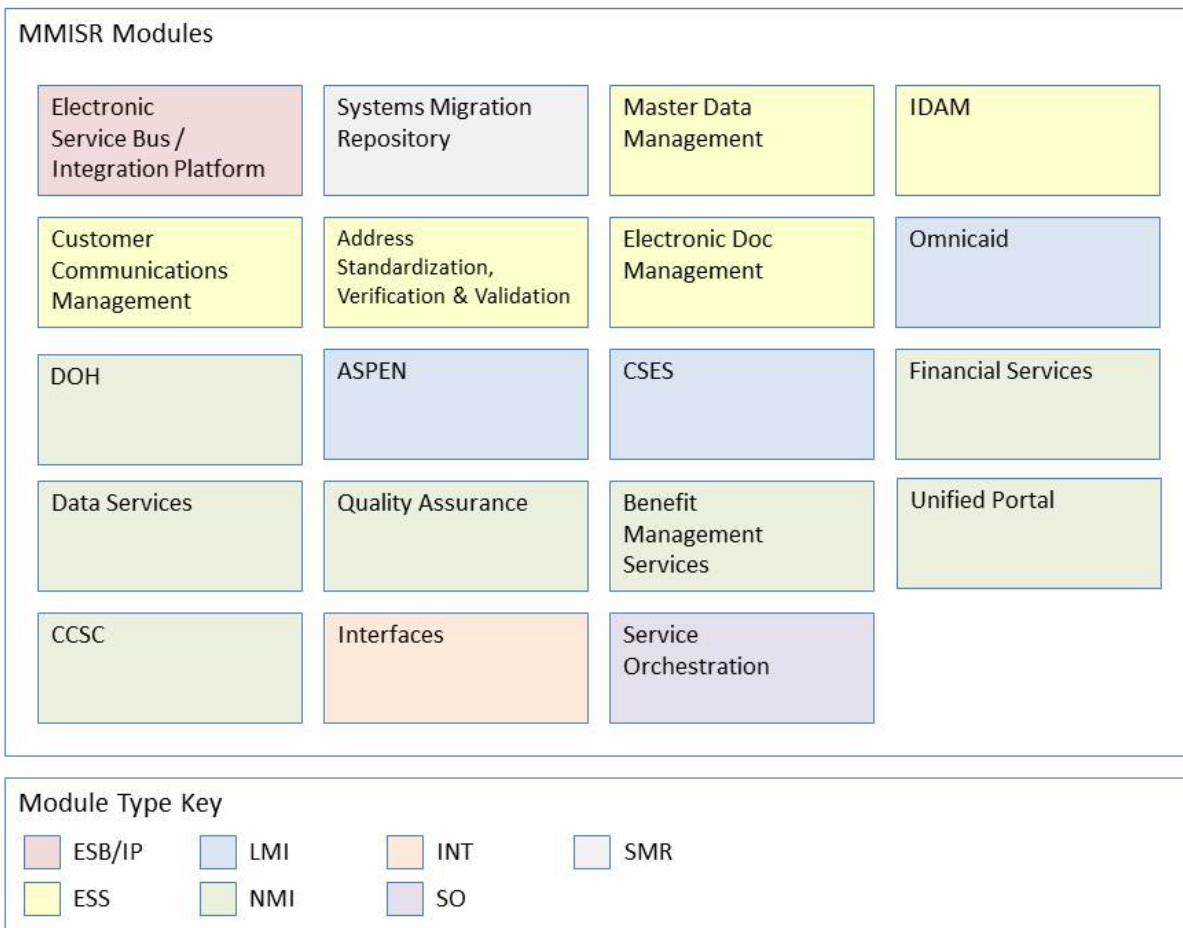Figure 3: MMISR Modules

2.2.1 MMISR Module Release Naming Convention

MMISR API and non-API module releases are uniquely identified using names determined by a module release naming convention. This convention includes a reference to the module itself (for example, MDM) and a three-digit version number (such as, X.Y.Z) where:

- X, Y, and Z are non-negative integers
- X, Y, and Z do not contain leading zeroes
- X represents the module's major version
- Y represents the module's minor version and must be reset to 0 when the release's major version is incremented (for example, 1.1.1 -> 2.0.0)
- Z represents the module's patch version and must be reset to 0 when the release's major or minor version is incremented (for example, 1.1.1 -> 2.0.0 or 1.1.1 -> 1.2.0)
- Each digit must increase numerically (for example, 1.0.0 -> 1.1.0 -> 1.1.1 -> 2.0.0 ...)

When a module release (for example, MDM 1.0.0) has been deployed to the MMISR production environment, the contents of that module release must not be modified. Any module release

modifications must be deployed to the MMISR production environment as a new module release (for example, MDM 1.0.1).

2.2.2 MMISR System Release Naming Convention

Similar to MMISR module releases, MMISR system releases are uniquely identified using names determined by a release naming convention. This convention includes a reference to the MMISR system itself (that is, MMISR) and a three-digit version number (such as, X.Y.Z) where:

- X, Y, and Z are non-negative integers.
- X, Y, and Z do not contain leading zeroes.
- X represents the MMISR system major version and must be incremented when one of more of the module release major version numbers are incremented.
- Y represents the MMISR system minor version.
 - Must be incremented when one or more of the modules release minor version numbers are incremented
 - Must be reset to 0 when the MMISR system release major version is incremented
- Z represents the MMISR system patch version.
 - Must be incremented when one or more of the modules release minor version numbers are incremented
 - Must be reset to 0 when the MMISR system release major or minor version is incremented
- Each digit must increase numerically (for example, 1.0.0 -> 1.1.0 -> 1.1.1 -> 2.0.0 ...).

When a MMISR system release (for example, MMISR 1.0.0) has been deployed to the production environment, the contents of its module releases must not be modified. Any module release modifications must be deployed to the production environment as a new MMISR system release (for example, MMISR 1.0.1) where the new MMISR system release number is a function of its module release numbers as described above.

The initial big-bang MMISR system production release will be named MMISR 1.0.0.


2.3 Planning Phase

The purpose of the planning phase is to:

- Identify a MMISR release's candidate project change requests (PCRs) and SDLC schedule.
- Present the MMISR release's candidate PCRs and SDLC schedule to the MMISR Change Control Board (CCB) for approval.
- Prepare a Release Baseline Plan (RBP).
- Present the RBP at a Release Baseline Review (RBR).

See the figure below for an overview of the planning phase.

Figure 4: Planning Phase



The following subsections describe the planning phase processes, reviews, and artifacts.

2.3.1 Prepare for Release CCB

The SI Contractor and module contractors, working with the State-led PMO, Business Transformation Council (BTC), Data Governance Council (DGC), Architecture Review Board (ARB), and NM HSD business owner identify candidate PCRs from the HHS 2020 Change Management Log to be delivered by an upcoming MMISR release based on the following criteria described in the MMISR CCMP:

- **Priority**
 - High: A critical change. Without this change, the MMISR system is not acceptable to stakeholders.
 - Medium: This priority level indicates a necessary but deferrable change, which makes the MMISR system less usable but still functional.
 - Low: A low priority level is a good change to have but the MMISR system functions acceptably without it.
- **Benefit of change:** Benefit of change to the NM HSD business owner
- **Risk if change not implemented:** Impact to the NM HSD business if the change is not implemented

Other criteria to be considered include:

- **Impact assessment:** The CCMP Impact Assessment Worksheet (IAW), completed for each PCR by the SI Contractor and module contractors, is critical for assessing the technical, data, and business process impacts of the change required to prepare the PCR's estimated level effort. The CCMP's IAW assesses impacts to:
 - Modules (including Interfaces)
 - Business processes
 - Stakeholders
- **Advisory board feedback:** Consultation feedback from the ARB, DGC, and BTC regarding the PCR's scope, compliance, and impact from a technical, data, and business process perspective.
- **Estimated level of effort:** The SI Contractor and module contractors estimated hours required to:
 - Analyze requirements
 - Design
 - Develop

- Test
- Implement
- Operate and maintain
- Document (for example, update MMISR SDLC deliverables)

PCRs involving architecture, data, and business processes changes will need to be reviewed by the ARB, DGC, and BTC, respectively. It is important the estimated level of effort for these PCRs account for these advisory board reviews.

- **Relationship to other PCRs:** If one or more PCRs affect the same MMISR system feature, it might make sense to implement these PCRs as part of the same release rather than as separate releases—thereby minimizing system development costs.
- **SI and module contractors available hours alignment:** The number of hours the SI Contractor and module contractors have available for the release’s requirements analysis, design, development, testing, implementation, and O&M where a release’s available hours must be greater than or equal to the sum of the release’s candidate PCR estimated levels of effort.
- **Scope alignment:** Is the change’s scope within the SI Contractor and module contractors’ scope?
- **Cost alignment:** Is the change’s cost within the SI Contractor and module contractors’ budget?
- **Schedule alignment:** Is the change’s schedule within the SI Contractor and module contractors’ schedule?

The following table identifies the three MMISR PCR categories.

Table 3: PCR Categories

Project Change Request Category	Definition
New feature	A MMISR change that delivers a new MMISR feature
Feature enhancement	A MMISR change that enhances an existing MMISR feature
Production defect fix	A MMISR change that fixes a MMISR production defect

2.3.1.1 Actors

The following table lists the actors, along with their roles and responsibilities, for the Prepare-for-Release CCB process.

Table 4: Prepare-for-Release CCB Process Actors

Actor	Responsibility
SI Contractor	• Identify candidate release PCRs. • Complete CCMP IAW.

Actor	Responsibility
	• Prepare PCR estimated level of effort. • Assess PCR relationship to other PCRs. • Identify SI Contractor release available hours. • Asses PCR alignment to SI Contractor contractual scope, budget, and schedule.
Module Contractors	• Identify candidate release PCRs. • Complete CCMP IAW. • Prepare PCR estimated level of effort. • Assess PCR relationship to other PCRs. • Identify module contractor release available hours. • Asses PCR alignment to module contractor contractual scope, budget and schedule.
State-led PMO	• Identify candidate release PCRs.
ARB	• Identify candidate release PCRs. • Review PCRs from a technical perspective.
BTC	• Identify candidate release PCRs. • Review PCRs from a business process perspective.
DGC	• Identify candidate release PCRs. • Review PCRs from a data perspective.
SI Change Manager	• Identify candidate release PCRs. • Present PCRs to advisory boards (that is, ARB, DGC, and BTC)
NM HSD Business Owner	• Identify candidate release PCRs.

2.3.1.2 Exceptions

1. Since release PCRs describe changes to a baseline release and the initial big-bang MMISR release (that is, MMISR 1.0.0) is the MMISR baseline release, there will be no MMISR 1.0.0 PCRs.

2.3.2 Conduct Release CCB

The SI Change Manager, in collaboration with the SI Contractor, module contractors, and State-led PMO, present the release's candidate PCRs to the CCB for their review and approval. If the CCB rejects

one or more of the PCRs then the SI Contractor and module contractors, working with the State-led PMO, BTC, DGC, ARB, NM HSD business owner, and SI Change Manager will identify and present replacement PCRs to the CCB. When the CCB approves all the release's PCRs, the SI Contractor and module contractors, in collaboration with the State-led PMO, can prepare the RBP to be presented at the RBR.

2.3.2.1 Process Activity

The following table identifies the entry criteria, input, process activities, exit criteria, and outputs for the "Conduct Release CCB" process.

Table 5: Conduct Release CCB Process Description

Entry Criteria	Input
• Candidate release PCRs identified • ARB, DGC, and BTC have reviewed each candidate release PCR • The following PCR criteria identified: ○ Priority ○ Benefit of change ○ Risk if change not implemented ○ Impact assessment ○ Advisory board feedback ○ Estimated level of effort ○ Relationship to other PCRs ○ SI Contractors and module contractors' available hours alignment ○ SI Contractor scope, cost, and schedule alignment ○ Module contractor scope, cost, and schedule alignment	• Candidate release PCRs • CCMP IAW for each candidate release PCR • Documented PCR criteria
Process Activity	
• The SI Change Manager, in collaboration with the SI Contractor, module contractors, and State-led PMO, present the release's candidate PCR(s) to the CCB for their review and approval. • If the CCB rejects one or more of the PCRs then the SI and module contractors, working with the State-led PMO, BTC, DGC, ARB, NM HSD business owner and SI Change Manager identify and present replacement PCRs to the CCB. To expedite the Conduct CCB process, the SI Change	

Manager should be prepared to present replacement release PCRs at the CCB for any PCRs rejected by the CCB. Once the CCB approves all the release's PCRs, the SI and module contractors, in collaboration with the State-led PMO, can prepare the RBP to be presented at the RBR	
Exit Criteria	Output
CCB approval of all release PCRs	CCB approved release PCRs

2.3.2.2 Actors

The following table lists the actors, along with their roles and responsibilities, for the "Conduct Release CCB" process.

Table 6: Actors Involved in Conduct CCB Meeting Process

Actor	Responsibility
SI Contractor	- Complete CCMP IAW. - Prepare replacement PCR estimated level of effort. - Assess replacement PCR relationship to other PCRs. - Asses replacement PCR alignment to SI Contractor contractual scope, budget, and schedule.
Module Contractors	- Complete CCMP IAW. - Prepare replacement PCR estimated level of effort. - Assess replacement PCR relationship to other PCRs. - Asses replacement PCR alignment to module contractor contractual scope, budget, and schedule.
ARB	Review replacement PCRs from a technical perspective.
BTC	Review replacement PCRs from a business process perspective.
DGC	Review replacement PCRs from a data perspective.
SI Change Manager	- Present PCRs to CCB. - Present replacement PCRs to advisory boards (that is, ARB, DGC, and BTC).
NM HSD Business Owner	Identify candidate release replacement PCRs.
CCB	Review and approve or disapprove candidate release PCRs.

2.3.3 Prepare RBP

The SI Contractor and module contractors, working with the State-led PMO, prepare an RBP. The RBP outlines the release's:

1. SDLC
2. Baseline scope (such as, PCRs)
3. Baseline schedule
4. Key stakeholder roles and responsibilities
5. Assumptions
6. Constraints
7. Risks

It serves as a reference of authority for the future of the release. The following provides a more detailed description of the RBP's contents:

- **SDLC:** An overview of the release's SDLC phases, reviews, and artifacts, specifically:
 - Planning phase
 - CCB meeting
 - RBP
 - RBR
 - Requirements analysis phase
 - Requirements Definition
 - Requirements Review
 - Design phase
 - Design document
 - Design review
 - Development phase
 - Application development verification
 - Test phase
 - Test Readiness Review
 - Test plans
 - Test reports
 - Implementation phase
 - Implementation Readiness Review
 - Implementation test plans
 - Implementation test reports
 - Operational Readiness Review
 - O&M phase
 - Operational test plans
 - Operational test reports
 - Production Readiness Review

- Post-implementation review
- **Scope:** The list of PCRs to be delivered by the release, specifically:
 - PCR Numbers
 - PCR Descriptions
- **Schedule:** The release’s SDLC dates for the following meetings, activities, and reviews:
 - Conduct CCB meeting.
 - Submit RBP.
 - Conduct RBR.
 - Submit requirements definition.
 - Conduct requirements review.
 - Submit design document.
 - Conduct design review.
 - Conduct application development verification.
 - Conduct test readiness review.
 - Submit test plans.
 - Submit test reports.
 - Conduct Implementation Readiness Review (IRR)
 - Submit implementation test plans
 - Submit implementation test reports
 - Conduct Operational Readiness Review (ORR)
 - Submit operational test plans
 - Submit operational test reports
 - Conduct Production Readiness Review
 - Conduct post-implementation review
- **Key stakeholder roles and responsibilities**
 - NM HSD Project Manager
 - NM HSD Business Owner
 - SI Contractor Implementation Manager
 - Module Contractor Project Managers
- **Assumptions, constraints, and risks:** List of the release’s assumptions, constraints, and risks

The SI Contractor is responsible for submitting the RBP to State-led PMO prior to conducting the RBR. See Appendix D: RBP Template for a SharePoint link to the MMISR project’s RBP template.

2.3.3.1 Actors

The following table lists the actors, along with their roles and responsibilities, for the “Prepare RBP” process.

Table 7: Prepare RBP Process Actors

Actor	Responsibility
SI Contractor	• Prepare the RBP. • Submit the RBP to the State-led PMO.
Module Contractor	• Prepare the RBP.

2.3.4 Conduct RBR

The SI Contractor and module contractors, in collaboration with the State-led PMO, conduct the RBR. The purpose of the RBR is for the SI Contractor and module contractors to kick off the release's system development with the State-led PMO and NM HSD business owner by reviewing the RBP, specifically the release's:

1. SDLC
2. Baseline scope
3. Baseline schedule
4. Key stakeholder roles and responsibilities
5. Assumptions
6. Constraints
7. Risks

With the State-led PMO and NM HSD business owner approval of the RBP at the RBR, the SI Contractor and module contractors, in collaboration with the State-led PMO and NM HSD business owner, start the requirements analysis phase, the second phase of the release's SDLC.

2.3.4.1 Process Activity

The following table identifies the entry criteria, inputs, process activities, exit criteria, and outputs for the "Conduct RBR" process.

Table 8: Conduct RBR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs

Entry Criteria	Input
• The release's SDLC, baseline scope, baseline schedule, key stakeholder roles and responsibilities, assumptions, constraints, and risks have been documented in the RBP and submitted to the State-led PMO and NM HSD business owner.	• RBP

Process Activity	
• The SI Contractor and module contractors, in collaboration with the State-led PMO, conduct the RBR. • The RBR kicks off the release's system development, which is facilitated by the SI Contractor and module contractors and is attended by the State-led PMO and NM HSD business owner. • The purpose of the RBR is to review the following release-related information documented in the RBP: ○ SDLC ○ Baseline scope ○ Baseline schedule ○ Key stakeholders including their roles and responsibilities ○ Assumptions ○ Constraints ○ Risks	
Exit Criteria	Output
• State-led PMO and NM HSD business owner approval of the RBP	• If the State-led PMO and NM HSD business owner approve the RBP, then the release shall be qualified to start the requirements analysis phase. • If not, then the release will be rejected for remediation.

2.3.4.2 Actors

The following table lists the actors, along with their roles and responsibilities, for the "Conduct RBR" process.

Table 9: Conduct RBR Process Actors

Actor	Responsibility
SI Contractor	• Conduct the RBR. • Remediate RBP issues identified by the State-led PMO and/or NM HSD Business Owner.
Module Contractors	• Conduct the RBR. • Remediate RBP issues identified by the State-led PMO and/or NM HSD Business Owner.

Actor	Responsibility
State-led PMO	Review and approve or disapprove the RBP.
NM HSD Business Owner	Review and approve or disapprove the RBP.

2.3.5 Planning Phase Exceptions

1. Since the scope and schedule for the initial big-bang MMISR release (that is, MMISR 1.0.0) have already been determined, the planning phase will not be executed for MMISR 1.0.0.
2. Executing the planning phase for patch releases might need to be expedited based on the patch's urgency. Expediting can involve emergency ARB, DGC, BTC, or CCB meetings.

See the MMISR CCMP for details regarding the change-management aspects of the planning phase.


2.4 Implementation Phase

The purpose of the implementation phase is to:

- Conduct an IRR to ensure the MMISR release has completed test phase testing and is ready for promotion to the user acceptance testing (UAT) and patch (production-like) environments for implementation phase testing.
- Promote the MMISR release to the UAT and patch (production-like) environments.
- Conduct implementation phase testing.
- Promote MMISR release to training environment.
- Conduct endUser training.
- Conduct O&M team training.
- Conduct an ORR to ensure:
 - MMISR release has undergone implementation phase testing and is ready to promote to the production and fail-over environments for operational testing and subsequent turnover to the O&M team and end users.
 - The O&M team has been trained on how to operate and maintain the MMISR release.
 - The end users have been trained on how to use the MMISR release.

See the figure below for an overview of the implementation phase.

Figure 5: Implementation Phase



The following subsections describe the implementation phase processes, reviews, and artifacts.

See the MMISR Test Management Plan for process details regarding the testing aspects of the implementation phase. See the MMISR Training Plan and Training Manual for details regarding the training aspects of the implementation phase.

2.4.1 Conduct Implementation Readiness Review

The IRR is conducted to determine if a MMISR release is ready to proceed from the test phase to the implementation phase by assessing the following:

1. Implementation testing objectives
2. Implementation testing methods and procedures
3. Scope of implementation testing
4. End-user training objectives
5. End-user training methods and procedures
6. End-user training scope
7. O&M team training objectives
8. O&M team training methods and procedures
9. O&M team training scope

The IRR also confirms the following:

1. Test phase results are complete and accurate.
2. Implementation phase test cases have been prepared.
3. Implementation phase test environments have been prepared.
4. Implementation phase test data has been prepared.
5. Implementation phase test resources are prepared.
6. Traceability of implementation phase test cases to the requirements.
7. End-user training materials have been prepared.
8. End-user training environment has been prepared.
9. End-user training data has been prepared.
10. End-user training resources are prepared.
11. O&M team training materials have been prepared.
12. O&M team training environment has been prepared.
13. O&M team training data has been prepared.
14. O&M team training resources are prepared.

2.4.1.1 Process Activity

The following table identifies the IRR entry criteria, inputs, process activities, exit criteria, and outputs.

Table 10: IRR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs

Entry Criteria	Input
• Test phase test-case execution is completed with no outstanding critical defects (See the Test Management Plan for defect severity criteria). • Test phase test reports are documented according to the Test Management Plan. • Implementation phase test cases, test data, resources, and environment are identified. • End-user training materials, resources, and environment are identified. • O&M team training materials, resources, and environment are identified.	• Test phase test-case and execution test reports • Implementation phase test cases and test data identified • End-user training materials • O&M team training materials
Process Activity	
The SI Contractor and module contractors will provide the following release evidence before proceeding to the implementation phase: • Test phase activities, including the test reports and metrics • Confirm the successful completion of test phase testing activities • End-user training materials, resources, and environment • O&M team training materials, resources, and environment The review board actors, listed in the Test Management Plan, review the evidence, inspect the quality of the test phase, prepare end-user training and O&M team training preparation activities, and qualify the MMISR release for the implementation phase.	
Exit Criteria	Output
• Test phase execution reports are reviewed and approved. • Mitigation strategy for open defects is established. • Implementation phase test cases and data are reviewed. • Implementation testing, end-user training, and O&M team training resources are ready.	• If the results of the review process are satisfactory, then the release shall be qualified for the implementation phase and promoted to the UAT and patch (production like) environments • If not satisfactory, then the release will be rejected for remediation.

• End-user training materials are reviewed. • O&M team training materials reviewed	
---	--

2.4.1.2 Actors

The following table lists the actors, along with their roles and responsibilities, for the “Conduct IRR” process.

Table 11: Conduct IRR Process Actors

Actor	Roles and Responsibilities
SI and Module Contractor Test Leads	• Present the evidence of test phase execution in the form of test reports and test cases. • Provide implementation phase test cases, data, and environment.
SI and Module Contractor Training Leads	• Provide end-user training materials and environment. • Provide O&M team training materials and environment.
SI and Module Contractor Project Managers and State-led PMO	• Oversee the IRR process.

2.4.2 Build-and-Deploy Implementation Test Environments

The release build-and-deploy process transforms source code files into an installable and distributable software release and installs the software release in the target environment. A deployed release is achieved by taking all the release’s relevant source code files, compiling them, creating build artifacts, and then installing those artifacts into the target environment. An effective build-and-deploy process helps the engineering team reduce the time and effort to deployment and update software releases in any given environment. As part of the implementation phase, releases are built and deployed to the implementation phase’s UAT and patch (production-like) environments.

2.4.2.1 Build/Deploy Types

The following table summarizes the build/deploy types and the use cases, where applicable.

Table 12: Build/Deploy Types

Build/Deploy Type	How Triggered
Periodic builds and deployments	• Triggered by a tool in an automated fashion set to run on a pre-configured interval, usually nightly for development integration

Build/Deploy Type	How Triggered
On-demand or manual builds and deployments	• Triggered manually • Includes a build of the source code for a planned or ad hoc (patch) release to quality assurance (QA) or a higher environment

2.4.2.2 Build/Deploy Tools

The tools associated with the build-and-deploy process are listed in the table below.

Table 13: Build/Deploy Tools

Tool	Usage
Atlassian Bitbucket	The Atlassian Bitbucket is a repository management solution based on the distributed version control system, Git. Bitbucket is used to store code repositories across the HHS 2020 enterprise solution.
Atlassian Bamboo	This build/deploy tool is used for continuous integration, deployment, and delivery.
SonarQube	SonarQube is a platform for continuous inspection of code quality. It is used to perform automatic reviews with static analysis of code to detect bugs, code smells, and security vulnerabilities on programming languages like Java.
SpotBug/PMD	This tool is a static code analyzer used to discover common programming flaws, such as bad practices, exception handling, cyclomatic complexity, and others.
Apache Maven	Apache Maven is a build-and-deploy automation tool used primarily for Java projects.
Apache Ant	Apache Ant is a build-and-deploy automation tool used primarily for Java projects.
Gradle	Gradle is an open-source build-and-deploy automation system that builds upon the concepts of Apache Ant and Apache Maven.

2.4.2.3 Process Activity


Every build-and-deploy is a multi-step process that contains the following steps:

- **Build Initiation:** Depending on the type of the build/deploy, the build-and-deploy process is initiated manually or periodically on a pre-configured interval. The build-and-deploy tool, Atlassian Bamboo, is hosted on a server called the build server.
- **Code Checkout:** The build-and-deploy tool checks out the source code from the Git-based distributed version control repository, Atlassian Bitbucket.
- **Code Compilation:** The code units are compiled, and the resultant artifacts are generated.
- **Test Suite Execution:** As a precondition for artifact generation, the unit/unit integration test suite is triggered, and code coverage is performed. This is enabled by an underlying build-

and-deploy automation tool, such as Apache Maven (listed in table 13 above). Test results are generated in the form of a report.

- **Code Quality Check:** The code quality checks are performed using SonarQube, SpotBug/PMD tools. The results are generated in the form of a report.
- **Artifact Generation:** The build artifacts (executable binaries) are generated and placed in the build server for further deployment to the run time environments.
- **Build Log Archival:** For post-build verification and troubleshooting purposes, the build logs are archived on the build server by the CI tool, Bamboo.
- **Prepare Version Descriptions:** Build and package engineers identify and record the exact version of the software prepared and deployed in each environment.
- **Build Notification:** The success or failure of the build-and-deploy process is communicated via emails in an automated fashion.

Figure 6: Build-and-Deploy Process Life Cycle

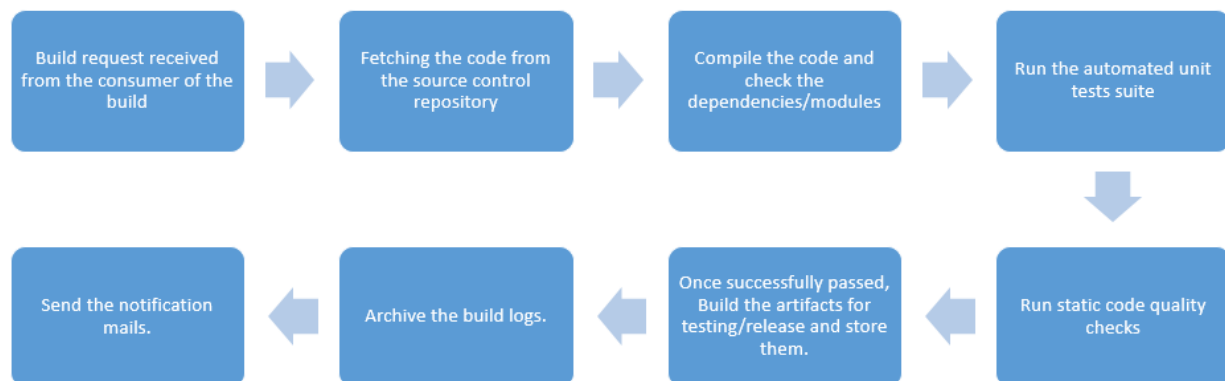

2.4.2.4 Actors

The following table lists the actors, along with their roles and responsibilities, for the “Build-and-Deploy Implementation Test Environments” process.

Table 14: Build-and-Deploy Implementation Test Environments Process Actors


Actor	Roles and Responsibilities
SI and Module Contractor Build-and-Deploy Engineers	Manages: • Build environment setup. • Build automation and configuration. • Build and deploy (manual). • Build artifact management.
SI and Module Contractor Infrastructure Engineers	• Responsible for setting up needed build infrastructure

Actor	Roles and Responsibilities
SI and Module Contractor Software Developers	Develops software, unit tests, and plans/consumes builds
SI and Module Contractor Testers	- Uses builds for verification activities - Manually deploys when required
SI and Module Contractor Project Managers	- Project planning and execution - Process approvals


2.4.2.5 Continuous Integration and Continuous Deployment

Continuous integration is a development practice that requires developers to integrate code into a source repository several times a day or nightly. Each check-in is then verified by an automated build, run unit test suites, and code quality checks that allow teams to detect problems in the early stages.

Figure 7: Continuous Integration

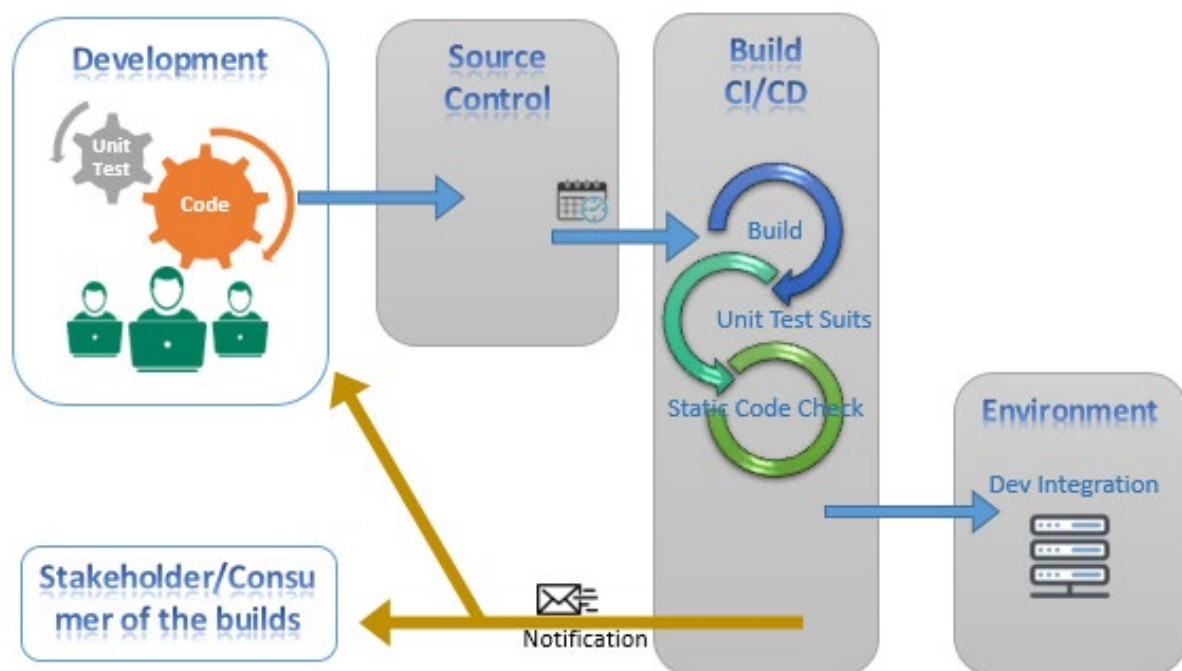

Continuous deployment is the process of keeping an application deployable at any point or even automatically releasing it for testing if the latest version passes all checks.

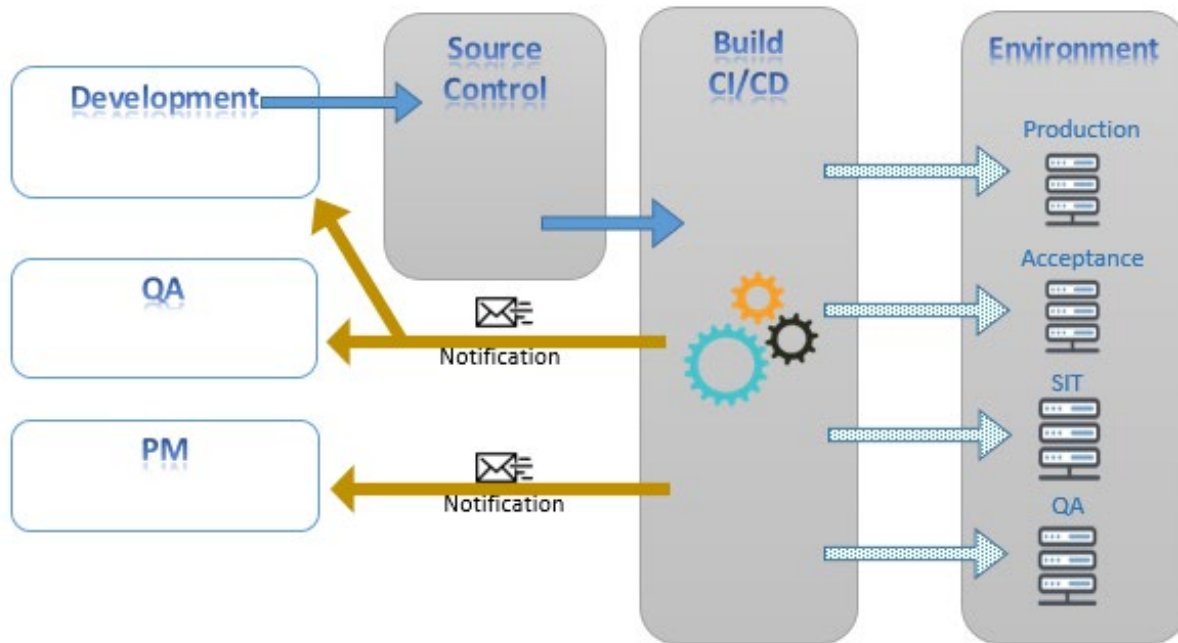Figure 8: Continuous Deployment

2.4.2.6 Exceptions

Some of the HHS 2020 systems rely on commercial off-the-shelf (COTS) products. Depending on the extent of the configuration and customization of the COTS products, the build process has already been explained, may not be applied because of the reasons listed below:

- **Product integration limitation:** Some COTS products are not meant to integrate with build tools like Bamboo nor do they generate artifacts compatible with these tools.
- **Configuration export between environments:** Some COTS products require configuration files to be exported in a proprietary format or Extensible Markup Language (XML). These configuration files are then imported into the COTS product installed in the higher environment.

2.4.3 Conduct Implementation Testing


Business application and infrastructure implementation testing functions are performed as part of implementation testing. Implementation testing is executed within the implementation phase's UAT and patch (production-like) environments.

The objective of implementation testing is to:

- Verify and validate the MMISR release behaves as required in UAT and patch (production-like) environments and that it is configured with the same infrastructure found in the target production environment.
- Confirm the security settings of the MMISR release comply with the System Security Plan (SSP).

The figure below illustrates the transition of the MMISR release through the stages of implementation testing. The agency approves the fully tested MMISR release to be promoted to the production environment based on the Agency Acceptance Test Report.

Figure 9: Implementation Testing

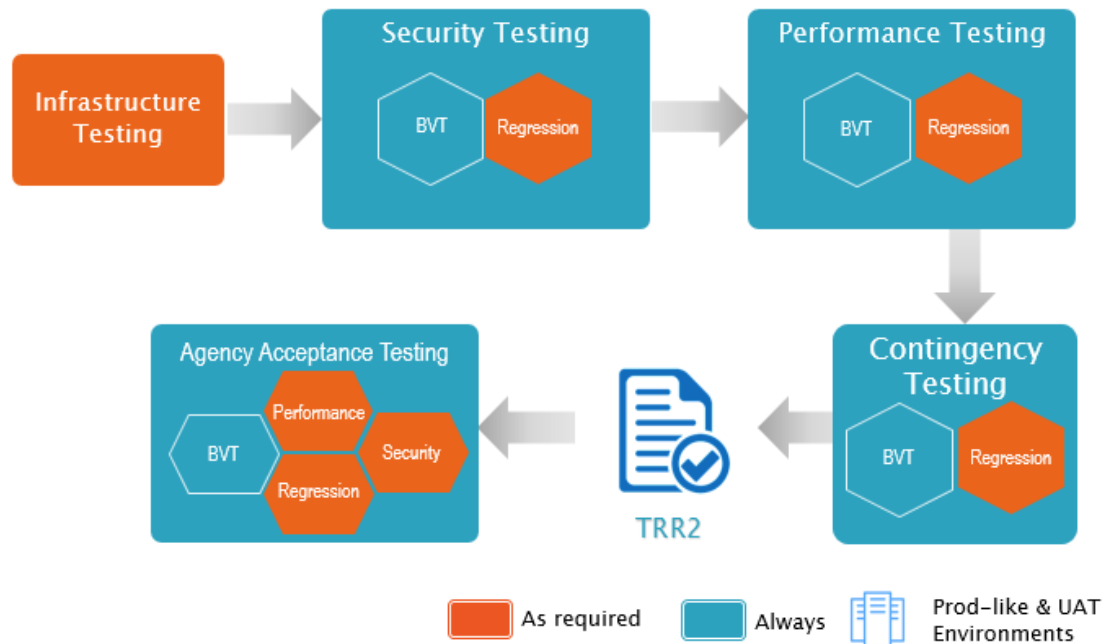

Implementation testing is comprised of the following testing stages:

- Infrastructure (platform) testing assesses the hardware installation, network connectivity and access, and software platform installation and configuration, as well as acting as a readiness check for production usage.
- Security testing to verify and validate that the processes, business application, software platform, and infrastructure complies with the Minimal Acceptable Risk Standards for Exchanges (MARS-E) security controls.
- Performance testing involves load and stress testing of the business application to ensure the application and the underlying platform is capable of handling the surge in requests in the production environment.
- Contingency testing is a critical test function performed before the application is ready for production use. The Initial Contingency Planning Testing ensures the notification and activation requirements and procedures are followed in a timely manner during a contingency.
- Agency Acceptance Testing is the phase in which the identified acceptance test cases are executed and validated by NM HSD. The results of Agency Acceptance Testing are presented to NM HSD in the form of Agency Acceptance Test Summary Reports.

2.4.3.1 Actors

The following table lists the actors, along with their roles and responsibilities, for the “Conduct Implementation Testing” process.

Table 15: Conduct Implementation Testing Process Actors

Actor	Responsibility
QA testers, infrastructure engineers, and project managers of all integrating partners	Collaboration for implementation testing

2.4.4 Build-and-Deploy Training Environment

The release build-and-deploy process transforms source code files into an installable and distributable software release and installs the software release in the target environment. A deployed release is achieved by taking all the release’s relevant source code files, compiling them, creating build artifacts, and then installing those artifacts into the target environment. An effective build-and-deploy process helps the engineering team reduce the time and effort to deploy and update software releases in any given environment. Only after receiving a release’s UAT signoff can the release be built and deployed to the training environment to support end-user and O&M team training. The same release build-and-deploy process described in the “Section 2.4.2 Build-and-Deploy Implementation Test Environments” process above is used to build and deploy the release to the training environment.

2.4.5 Conduct End-User Training

The Training Plan and Training Manual will provide a detailed description of the MMISR “Conduct End-User Training” process. These documents will describe how MMISR business component end-user business processes will need to be modified to accommodate the new business and technology changes introduced by the release. This section of the RSP provides an overview of the “Conduct End-User Training” process.

2.4.5.1 Process Activity

The following table identifies the “Conduct End-User Training” entry criteria, inputs, process activities, exit criteria, and outputs.

Table 16: Conduct End-User Training Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs

Entry Criteria	Input
- Release deployed to training environment - Release-specific end-user training materials reviewed by the SI Training Manager - Release Training Plan prepared by the module contractors identifying the	- Training environment - Release-specific end-user training materials to address the new business and/or technology changes introduced by the release in the form of:

release's overall training goals, learning objectives, and activities reviewed by the SI Contractor Training Manager • Release Training Calendar prepared and communicated through SharePoint and email distribution to allow time for course registration and preparation of training materials	○ User manuals ○ Training aids ○ Tip sheets ○ Training videos ○ Training meeting agendas • Release Training Plan • Release Training Calendar
Process Activity	
The SI Contractor and module contractors shall • Provide additional and updated end-user training materials in the form of: ○ User manuals ○ Training aids ○ Tip sheets ○ Training videos ○ Training meeting agendas • Support end-user training delivery to address the new business and technology changes introduced by the release. • Prepare a Release Training Calendar to be provided and communicated through SharePoint and email distribution. • Incorporate, in its training delivery, a competency-based train-the-trainer-based program designed to assist knowledge transfer and end-user performance. • Record all completed release-based training in the training logs.	
Exit Criteria	Output
• End-user trainers trained on new business and technology changes introduced by the release	• Updated end-user trainer release-based training logs

2.4.5.2 Actors

The following table lists the actors, along with their roles and responsibilities, for the “Conduct End-User Training” process.

Table 17: Conduct End-User Training Process Actors

Actor	Responsibility
SI Contractor Training Manager and Staff	- Oversee the development and delivery of the module contractors' release-specific end-user training materials. - Review and approve release-specific end-user training materials prompted by the introduction of the release. - Prepare a Release Training Calendar. - Ensure training log updates.
Module Contractors Training Manager and Staff	- Review and approve release-specific end-user training materials prompted by the introduction of the release. - Conduct release-specific end-user training. - Update the training logs.
State-led PMO	Review and approve end-user training materials prompted by the introduction of the release.
End User Trainers	Complete release specific end-user training

2.4.6 Conduct O&M Team Training

The Training Plan and Training Manual will provide a detailed description of the “Conduct O&M Team Training” process. These documents will describe how MMISR release O&M processes will need to be modified to accommodate the changes introduced by the release. This section of the RSP provides an overview of the “Conduct O&M Team Training” process.

2.4.6.1 Process Activity

The following table identifies the “Conduct O&M Team Training” entry criteria, inputs, process activities, exit criteria, and outputs.

Table 18: Conduct O&M Training Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs

Entry Criteria	Input
- Release deployed to training environment - Release-specific training materials reviewed by the SI Training Manager - Release Training Plan prepared by the module contractors identifying the	- Training environment - Release-specific O&M team training materials to address the new business and/or technology changes introduced by the release in the form of: - User manuals

release's overall training goals, learning objectives, and activities reviewed by the SI Contractor Training Manager • Release Training Calendar prepared and communicated through SharePoint and email distribution to allow time for course registration and preparation of training materials	○ Training aids ○ Tip sheets ○ Training videos ○ Training meeting agendas • Release Training Plan • Release Training Calendar
Process Activity	
The SI Contractor and module contractors shall: • Provide additional and updated O&M team training materials in the form of: ○ User manuals ○ Training aids ○ Tip sheets ○ Training videos ○ Training meeting agendas • Support O&M team training delivery to address the new business and technology changes introduced by the release. • Prepare a Release Training Calendar to be provided and communicated through SharePoint and email distribution. • Incorporate, in its training delivery, a competency-based train-the-trainer based program designed to assist knowledge transfer and O&M team performance. • Record all completed release-based training in the training logs.	
Exit Criteria	Output
• O&M team trainers trained on new business and technology changes introduced by the release	• Updated O&M team trainer release-based training logs

2.4.6.2 Actors

The following table lists the actors, along with their roles and responsibilities, for the “Conduct O&M Team Training” process.

Table 19: Conduct O&M Training Process Actors

Actor	Responsibility
SI Contractor Training Manager and Staff	• Oversee the development and delivery of the module contractors' release specific O&M team training materials.

Actor	Responsibility
	- Review and approve release-specific O&M team training materials prompted by the introduction of the release. - Prepare a Release Training Calendar. - Ensure training logs are updated.
Module Contractors Training Manager and Staff	- Review and approve release-specific O&M team training materials prompted by the introduction of the release. - Conduct release-specific O&M team training. - Update training logs.
State-led PMO	Review and approve O&M team training materials prompted by the introduction of the release.
O&M Team Trainers	Complete release-specific O&M team training.

2.4.7 Conduct Operational Readiness Review

The ORR is conducted to determine if a MMISR release is ready to proceed from the implementation phase to the O&M phase.

The ORR assesses the following:

1. Operational testing objectives
2. Operational testing methods and procedures
3. Scope of operational testing

The ORR also confirms the following:

1. Implementation phase test results are complete and accurate.
2. Agency acceptance testing signoffs have been submitted.
3. O&M phase test cases have been prepared.
4. O&M phase test data has been prepared.
5. O&M phase test resources are prepared.
6. Traceability of O&M phase test cases to the requirements
7. End users' trainers have been trained.
8. O&M team trainers have been trained.

2.4.7.1 Process Activity

The following table identifies the ORR entry criteria, inputs, process activities, exit criteria, and outputs.

Table 20: ORR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs

Entry Criteria	Input
• Implementation phase test case execution is completed with no outstanding critical defects (see Test Management Plan for defect severity criteria) • Implementation phase test reports are documented according to the Test Management Plan • End user trainers are trained • O&M team trainers are trained	• Implementation phase test execution test reports • End-user trainer training test results • O&M team trainer training test results • O&M phase test cases and test data identified
Process Activity	
All participating module contractors will provide the following evidence before proceeding to the O&M phase: • Implementation test activities, including the test reports and metrics, confirming the successful completion of implementation testing activities • End-user train-the-trainer training results • O&M team train-the-trainer training results The review board actors, listed in the Test Management Plan, shall then review the evidence, inspect the quality of the implementation testing, review the end-user and O&M team train-the-trainer test results, and qualify the MMISR release for the O&M phase.	
Exit Criteria	Output
• Implementation phase test execution reports are reviewed and approved • Mitigation strategy for open defects is established • O&M phase test cases and data reviewed • End-user train-the-trainer test results reviewed • O&M team train-the-trainer test results reviewed	• If the results of the review process are satisfactory, then the release shall be qualified for the O&M phase and promoted to the production and disaster recovery environments. • If not satisfactory, then the release will be rejected for remediation.

2.4.7.2 Actors

The following table lists the ORR actors, along with their roles and responsibilities, for the “Conduct Operational Readiness Review” process.

Table 21: Conduct Operational Readiness Review Process Actors


Actor	Roles and Responsibilities
SI and Module Contractor Test Leads	• Present evidence of Implementation phase test execution in the form of test reports and test cases. • Provide O&M phase test cases, data, and environment.
SI and Module Contractor Training Leads	• Present evidence of end-user training. • Present evidence of O&M team training.
SI and Module Contractor Project Managers and State-led PMO	• Oversee the ORR process.

2.5 O&M Phase

The purpose of the O&M phase is to:

- Build and deploy the release to the production and disaster recovery environments.
- Conduct operational testing.
- Conduct a Production Readiness Review (PRR) to ensure the MMISR release has undergone operational testing and is ready to be turned over to the O&M team and end users.
- Operate and maintain the release in the production environment.
- Conduct a Post Implementation Review (PIR) to identify release lessons learned.

The figure below provides an overview of the O&M phase.

Figure 10: O&M Phase

The following subsections describe the release O&M phase processes, reviews, and artifacts.

See the MMISR Test Management Plan for process details regarding the testing aspects of the O&M phase. See the O&M Plan, Information Technology Service Management (ITSM) Standup, and O&M Manual for process details regarding the operation and maintenance aspects of the O&M phase. See the MMISR Quality Management Plan for quality management aspects of the O&M phase.

2.5.1 Build-and-Deploy Production Environments

The build-and-deploy process transforms source code files into an installable and distributable software release and installs the software release in the target environment. A deployed release is achieved by taking all the release's relevant source code files, compiling them, creating build artifacts, and then installing those artifacts into the target environment. An effective build-and-deploy process helps the engineering team reduce the time and effort to deploy and update software releases in any given environment. Only after receiving approval at the release's ORR can the release be built and deployed to the production and disaster recovery environments. The same release build-and-deploy process, described above in Section 2.4.2 Build-and-Deploy Implementation Test Environments, is used to build and deploy the release to the production and disaster recovery environments.

2.5.1.1 Exceptions

Planned Production Outage Notifications: Planned production outage notifications are used to notify stakeholders and groups of a planned MMISR production outage due to a MMISR release production deployment. The SI Contractor, in collaboration with the module contractors, State-led PMO, and NM HSD business owner, will prepare and email planned production outage notifications to a "to be determined" distribution list of MMISR stakeholders and groups two weeks, one week, and one day before the outage as well as the day of the outage. A draft version of the release notes will be included as an attachment to the notification. The release notes will focus on explaining the release's user interface related capabilities. The table below represents a sample planned production outage notification. See Appendix E for a sample of the NM HSD Release Notes, which will be used as a guide for preparing MMISR release notes.

Table 22: Sample MMISR Production Outage Notification

On Saturday, January 2, 2021, MMISR 1.1.0 will be deployed to the production environment. The deployment is scheduled to start at 8:00 AM MT and be completed by 5:00 PM MT. During the deployment, MMISR will be unavailable in the production environment. A MMISR 1.1.0 production go-live notification will be emailed to this notification's distribution when the deployment has been completed. MMISR 1.1.0 delivers the new features and improvements listed by module below and described in detail in the attached draft version of the MMISR 1.1.0 Release Notes.		
MMISR 1.1.0 Module Release	PCR #	Features/Improvements Description
MDM 1.1.0	35746	Master Employer Data – match and integrate source records and identifiers from disparate systems to create a master employer record containing the most current data from all matched systems for each employer and create a unique identifier for employer.
ESB 1.1.0	35733	Provide structured exception and error handling.

As a reminder, all MMISR production issues should be reported to the MMISR Help Desk. Their contact information is as follows:

Phone: <<TBD>>

Email: <<TBD>>

Thank you,

The NM HSD MMISR Team

Build-and-Deploy Release in Production Environment Communications: To facilitate SI Contractor, module contractor, and State-led PMO communications during the MMISR production deployment, a conference bridge will be available for the duration of the “Build-and-Deploy Production Environments” process as well as the “Conduct Operational Testing” and “Conduct Production Readiness Review” processes described below.

2.5.2 Conduct Operational Testing

The MMISR Test Management Plan describes the “Conduct Operational Testing” process. This subsection provides an overview of this process.

Operational testing confirms that the MMISR release is operational according to architectural and technical requirements in the production environment. The objective of operational testing is to verify the operational integrity, effectiveness, and resilience of the MMISR release in the production environments.

Operational testing is comprised of the following testing phases:

- Infrastructure testing assesses the hardware installation, network connectivity and access, and software platform installation and configuration as well as its readiness check for production usage.
- Production readiness testing is a breadth verification test (BVT) suite prepared exclusively for a production readiness check, to confirm the application has been installed and configured correctly in the production environment and is ready for operational use.
- Operational security testing verifies and validates that the processes, business application, software platform, and infrastructure complies with the MARS-E security controls.
- Operational contingency testing is a critical test function performed on the application deployed in the production environment. The Operational Contingency Planning Testing is performed to ensure the notification and activation requirements and procedures are followed in a timely manner during a contingency.
- Monitoring and reliability testing will ensure operational availability of the MMISR release and infrastructure by continuous monitoring of performance, incidents, and capacity utilization.

The figure below illustrates the transition of a MMISR release through the stages of operational testing:

Figure 11: Operational Testing

2.5.2.1 Actors

The following table lists the actors and their roles and responsibilities for the “Conduct Operational Testing” process.

Table 23: Actors of Operational Testing

Actor	Responsibility
QA testers, infrastructure engineers, application support engineers, and project managers of all integrating partners	Collaboration for operational testing

2.5.3 Conduct Production Readiness Review

The Production Readiness Review (PRR) is conducted to determine if a MMISR release is ready to be turned over to O&M team and end users.

The PRR confirms the following:

1. O&M phase test results are complete and accurate
2. O&M team has the appropriate start-up and shutdown scripts, accurate application architecture documentation, application validation procedures, and valid contact information to ensure operability of the MMISR release

2.5.3.1 Process Activity

The following table identifies the PRR entry criteria, inputs, process activities, exit criteria, and outputs.

Table 24: PRR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs

Entry Criteria	Input
Operational test case execution is completed with no outstanding critical defects (see Test Management Plan for defect severity criteria)	Operational test case and execution test reports

Operational test reports are documented according to the Test Management Plan	
Process Activity	
All participating module contractors will provide the following evidence before the MMISR release is turned over to the O&M team and end users: Operational testing activities, including the test reports and metrics confirming the successful completion of operational testing activities The review board actors, listed in the Test Management Plan, shall then review the evidence, inspect the quality of the operational testing and qualify the MMISR release for production readiness.	
Exit Criteria	Output
- Operational test execution reports are reviewed and approved - Mitigation strategy for open defects is established	- If the results of the review process are satisfactory then the release shall be qualified for turnover to the O&M team and end users. - If not satisfactory, then the release will be rejected for remediation.

2.5.3.2 Actors

The following table lists the actors along with their roles and responsibilities for the Conduct Production Readiness Review process.

Table 25: Conduct Production Readiness Review Actors

Actor	Roles and Responsibilities
SI and Module Contractor Test Leads	Present evidence of O&M phase test execution in the form of test reports and test cases.
SI and Module Contractor Operations Managers	Present evidence of O&M processes to ensure operability of the MMISR release.
SI and Module Contractor Project Managers and State-led PMO	Oversee the PRR process.

2.5.4 Operate and Maintain in Production

The O&M Plan, ITSM Standup, and O&M Manual will provide a detailed description of the Operate and Maintain in Production process. This section of the RSP provides an overview of this process.

Multi-contractor environments pose significant operational and maintenance challenges which require an overarching ITSM framework made up of processes that clearly identify roles, responsibilities, service level agreements (SLAs) and key performance indicators (KPIs) for all ITSM areas for ensuring optimal release availability, performance and reliability. The SI Contractor will execute a service operations strategy according to the CMS XLC and ITSM framework to support:

- Coordinating ongoing problem identification, root cause analyses, and resolutions for problems that may not clearly fall within a single module contractor's domain of a MMISR release
- Monitoring progress in addressing problems that adversely affect MMISR release operations, service delivery, performance levels, and data integrity, in collaboration with the State-led PMO, module contractors, and stakeholders to ensure problems are being addressed within agreed-upon timeframes
- Assessing trends (for example, recurring problems within specified time frames) and making recommendations to help avert problem continuation or recurrence
- Working with the State-led PMO to monitor compliance with SLAs across the MMISR release. This will be accomplished through the use of automated tools and tracking as well as other data gathering, and reporting approaches agreed upon with NM HSD.
- Leveraging ITIL V3 service-level management and using SLAs to govern relationships between module contractors
- Evaluating and providing metrics to MMISR leadership related to SLA oversight of the module contractors
- Maintaining and updating performance management processes and policies for the Medicaid enterprise while ensuring the release conforms to NM HSD requirements
- Establishing release operations monitoring standard operating procedures according to ITSM guidelines and HHS 2020 guidelines
- Establishing release event, access, and problem management standard operating procedures in accordance with ITSM guidelines and HHS 2020 guidelines
- Working with the module contractors to establish a consolidated maintenance schedule for the release
- Working with the State-led PMO and module contractors to develop incident classification guidelines to be configured in the incident classifications in the enterprise ticketing system
- Working with the module contractors and State-led PMO to develop severity-based distribution lists to notify effected stakeholders during system outages
- Developing an O&M Manual that describes items such as startup, shutdown, maintenance, and troubleshooting procedures for release components
- Identifying tools and processes for monitoring performance of the release against performance criteria
- Monitoring the release by reviewing application log files and by using performance monitoring tools embedded within Oracle Fusion

- Managing and controlling the daily operational activities related to existing release modules and when establishing new or updated module connections
- Maintaining and enhancing the Medicaid enterprise process documentation, including the O&M Manual and providing operational process documentation for use by the Medicaid enterprise stakeholders
- Providing and staffing Tier-1 and Tier-2 service desks, which are operational 24 hours per 365 days per year
- Providing Tier-3 support for the SI module
- Coordinating module contractor Tier-3 activities
- Managing all aspects of system availability and disaster recovery

The O&M Manual will outline all aspects of the Service Operations, such as:

- Standard processing procedures
- Processing sequence
- Input/output procedures
- Production control procedures
- Monitoring procedures
- Diagnostic and problem handling procedures
- Backup and recovery procedures
- Shutdown and restart procedures
- Maintenance procedures
- Database and data administration procedures
- Configuration management
- Module contractor SLA information including Integrated Master Schedule (IMS) activities and deliverables

2.5.4.1 Actors

The following table lists the actors, along with their roles and responsibilities, for the “Operate and Maintain in Production” process.

Table 26: Operate and Maintain in Production Process Actors

Actor	Responsibility
SI Contractor Operations Manager	• Oversee the execution of all processes defined in the release O&M Manual. • Ensure the release O&M Manual processes are clearly defined, updated, and maintained.

Actor	Responsibility
	- Oversee the execution of all processes defined in the module release O&M Manual. - Ensure the module release O&M Manual processes are clearly defined, updated, and maintained.
Module Contractor Operations Managers	- Oversee the execution of all processes defined in the module release O&M Manual. - Ensure the module release O&M Manual processes are clearly defined, updated and maintained.
State-led PMO	- Oversee the execution of all processes defined in the release and module release O&M Manual. - Ensure the release and module release O&M Manual processes are clearly defined, updated, and maintained.

2.5.5 Conduct Post Implementation Review

The PIR is conducted no later than six months after the release's production go-live to:

1. Ascertain the degree of success from the MMISR release; the extent to which it met its objectives, delivered planned levels of performance, and addressed the specific requirements as originally defined.
2. Enable the MMISR team to learn lessons from the MMISR release's implementation to improve future MMISR release implementations.

In that context, the PIR examines whether the MMISR team achieved the results it planned for, what those results actually were, and what caused the results to be different from those planned for (if they are different).

2.5.5.1 Process Activity

The following table identifies the PIR entry criteria, inputs, process activities, exit criteria, and outputs.

Table 27: PIR Entry Criteria, Inputs, Process Activities, Exit Criteria, and Outputs

Entry Criteria	Input
No later than six months after release's production go-live	- Release project management lessons learned - Release system development lessons learned - Release certification lessons learned
Process Activity	

PIR participants present lessons learned related to the MMISR release's project management, system development, and certification processes. All lessons learned are input in the MMISR project SharePoint lessons learned log by the SI Contractor QA Manager.	
Exit Criteria	Output
N/A	MMISR SharePoint lessons learned log updates

2.5.5.2 Actors

The following table lists the actors along with their roles and responsibilities for the Conduct Post Implementation Review process.

Table 28: Conduct Post Implementation Review Process Actors

Actor	Roles and Responsibilities
SI and Module Contractor Project Managers and State-led PMO	• Presents MMISR release lessons learned, particularly those related to the release's project management processes
Requirement Leads • NM HSD • SI Contractor • Module Contractor	• Presents MMISR release lessons learned, particularly those related to the release's requirements analysis processes
Development Leads • NM HSD • SI Contractor • Module Contractor	• Presents MMISR release lessons learned, particularly those related to the release's design and development processes
Test Leads • NM HSD • SI Contractor • Module Contractor	• Presents MMISR release lessons learned, particularly those related to the release's testing processes
Implementation Leads • NM HSD • SI Contractor • Module Contractor	• Presents MMISR release lessons learned, particularly those related to the release's implementation processes
O&M Leads • NM HSD • SI Contractor	• Presents MMISR release lessons learned, particularly those related to the release's O&M processes

Actor	Roles and Responsibilities
Module Contractor	
SI Contractor QA Manager	- Facilitates the PIR - Inputs lessons learned into the MMISR SharePoint lessons learned log
Certification Manager	Presents MMISR release lessons learned, particularly those related to the release's certification processes
IV&V and Other Stakeholders	Presents MMISR release lessons learned related to the release's system development, certification and project management processes

2.6 Module Contractor Release Strategy Oversight

The SI Contractor has release strategy oversight responsibilities for the module contractors. The following subsections describe these responsibilities.

2.6.1 Planning Phase Oversight

The SI Contractor will oversee the module contractors' execution of the Planning Phase processes described above. Specific oversight responsibilities include:

1. Ensuring module contractors' preparedness prior to the CCB by reviewing their CCB inputs and entry criteria
2. Ensuring module contractors' preparedness prior to the RBR by reviewing their RBR inputs and entry criteria

2.6.2 Implementation Phase Oversight

The SI Contractor will oversee the module contractors' execution of the implementation phase processes described above. Specific oversight responsibilities include:

1. Ensuring module contractors' preparedness prior to the IRR by reviewing their IRR inputs and entry criteria
2. Ensuring module contractors' preparedness prior to the ORR by reviewing their ORR inputs and entry criteria
3. Providing oversight to the module contractors as they develop release specific training for the end users and O&M team

2.6.3 O&M Phase Oversight

The SI Contractor will oversee the module contractors' execution of the O&M phase processes described above. Specific oversight responsibilities include:

1. Ensuring module contractors' preparedness prior to the PRR by reviewing their PRR inputs and entry criteria
2. Ensuring module contractors' preparedness prior to the PIR by reviewing their PIR inputs and entry criteria

2.7 Release Scope

This section describes the high-level scope of the initial big-bang MMISR R1.0.0 modules scheduled to go-live in the production environment in 2021. The following SI Contractor requirement definition, interface management and service orchestration management deliverables will describe the MMISR R1.0.0 detailed scope in detail:

1. Requirements Definition Document – ESB and Orchestration Modules of the Platform
2. Requirements Definition Document – SMR
3. Requirements Definition Document – MDM
4. Requirements Definition Document – CCM
5. Requirements Definition Document – Address Standardization
6. Requirements Definition Document – Security (IdAM)
7. Requirements Definition Document – EDM
8. Requirements Definition Document – ASPEN
9. Requirements Definition Document – CSES
10. Requirements Definition Document – DoH
11. Requirements Definition Document – Data Services Integration
12. Requirements Definition Document – Quality Assurance Integration
13. Requirements Definition Document – BMS Integration
14. Requirements Definition Document – UPI Integration
15. Interface Management Plan
16. Interface Management Activities
17. (Service) Orchestration Management Plan
18. (Service) Orchestration Management Services

The following table contains the SI Contractor statement of work (SOW) descriptions for each of these deliverables.

**Table 29: MMISR R1.0.0 Module Release Scope**

MMISR R1.0.0 Module Release	Scope
ESB 1.0.0	SI SOW Requirements Definition – ESB and Orchestration Components of the Platform Description The contractor shall coordinate with HHS stakeholders to document requirements for service orchestration for transaction flows between the HHS2020 modules, applications and modules. General areas of requirements include, as described in the RFP, but at not limited to: 1. Manage, monitor and control routing, integrity and security of message exchanges; 2. Resolve contention between communicating service modules; 3. Enforce versioning of services and messages and the proper retirement of outdated services; 4. Implement and manage common services, such as logging/auditing services, event handling, data transformation and mapping and message and event queuing and sequencing; 5. Provide structured exception and error handling; 6. Provide protocol conversion; 7. Enforce communication service quality; 8. Enforce policies such as Service Level Agreements, security, service retries and others as the Vendor recommends 9. Implement other SOA best practices for service and message management. a. Secure and ensure the integrity of State information flowing through the Solution; b. Use Single Sign-on (SSO) and Identity and Access Management (IdAM) to implement Authentication, Authorization and Auditing; establish, integrate and manage unique logon IDs and security profiles for Stakeholders, Users and other Contractors seeking access to the MMISR; c. Use a state-produced Active Directory for State employees for full integration of managing user access to all SI modules and is based on Active Directory security groups so that, for State employees, there is no secondary user management within SI modules; and ii. Use IdAM for all other users; d. Facilitate integration with access to services for data sharing between applications and entities, in accordance with service contracts and security policies;

MMISR R1.0.0 Module Release	Scope
	e. Provide for successful integration of APIs when service interfaces are not available/feasible; f. Support automated and integrated service checkpoints to monitor service accuracy and completeness before proceeding to the next step or application batch process; g. Identify and use standards, protocols and methodologies to develop, maintain and execute privacy and security audit processes, procedures and audit trail information and restrict access when anomalies are detected; h. Provide the ability to suspend processing of erroneous transactions until the error is resolved and provide notification of the error and resolution; i. Monitor usage and maintain a record of resource levels and consumption within the Solution; j. Provide a central log of all problems and errors that includes error statistics by service, message, transaction and source; k. Distinguish between errors (stop process) and exception conditions (skip transaction and continue process); l. Perform SOA-related business process and service management; m. Capture performance data (e.g., elapsed time, dates) to support continuous improvement; and n. Support common SOA and Enterprise integration patterns, including publish/subscribe, broadcast, intermediaries, splitter/aggregator, parsing and validating messages and others as recommended by the Vendor.
SMR 1.0.0	SI SOW Requirements Definition – Systems Migration Repository Description The contractor shall coordinate with HHS stakeholders to document requirements create a SMR that will provide a robust, yet secure, environment for migrating data from source and legacy systems (i.e., <u>Omnicaid</u> and <u>ASPEN</u>) into the HHS 2020 Framework. The SMR will consume copies of entire databases, files and other types of extracted data, put those data into repositories, measure and improve data quality and make those data available in an approved format (schema) to systems inside the HHS 2020 Enterprise. General areas of requirements include, as described in the RFP, but at not limited to: 1. Must preserve the integrity of source systems' data (structure, constraints, keys and values), and employ processes and tools that stage, cleanse and organize data before it is made available to other HHS 2020 systems and services. Once in the SMR, data integrity, including referential and foreign integrity must be maintained;

MMISR R1.0.0 Module Release	Scope
	2. Must comply with all applicable business, Federal and State compliance security requirements; 3. Must include a metadata repository that provides descriptions of source data structures, formats and definitions and mappings to target HSD 2020 Information Architecture schemas; 4. Use effective-dated transactions and table updates, either future dated or retroactive, with the ability to specify data edits by transaction type as required to maintain data and transaction integrity within the SMR; 5. Audit and reconcile all imported and exported data and that provides automatic program checks to verify correct processing and data integrity; 6. Support physical-to-logical model mapping and rationalization and provide ability to define model-to-model relationships among repository objects, data models and data flows via graphical, attribute level mapping; 7. Extend and share metadata bi-directionally with other tools and through automated synchronization of metadata across multiple instances of the tools; 8. Support multiple secure environments required for SMR and for the MMISR (e.g., development, test, production); and 9. Enable role-based security, security to the attribute level of the database, audit trails and safe storage and handling of data in accordance with all applicable security requirements.
SMR 2.0.0	SI SOW Requirements Definition – Systems Migration Repository Description The contractor shall coordinate with HHS stakeholders to document requirements create a SMR that will provide a robust, yet secure, environment for migrating data from source and legacy systems (i.e., <u>CSES</u> and <u>DOH</u>) into the HHS 2020 Framework. The SMR will consume copies of entire databases, files and other types of extracted data, put those data into repositories, measure and improve data quality and make those data available in an approved format (schema) to systems inside the HHS 2020 Enterprise. General areas of requirements include, as described in the RFP, but at not limited to: 1. Must preserve the integrity of source systems' data (structure, constraints, keys and values), and employ processes and tools that stage, cleanse and organize data before it is made available to other HHS 2020 systems and services. Once in the SMR, data integrity, including referential and foreign integrity must be maintained;

MMISR R1.0.0 Module Release	Scope
	2. Must comply with all applicable business, Federal and State compliance security requirements; 3. Must include a metadata repository that provides descriptions of source data structures, formats and definitions and mappings to target HSD 2020 Information Architecture schemas; 4. Use effective-dated transactions and table updates, either future dated or retroactive, with the ability to specify data edits by transaction type as required to maintain data and transaction integrity within the SMR; 5. Audit and reconcile all imported and exported data and that provides automatic program checks to verify correct processing and data integrity; 6. Support physical-to-logical model mapping and rationalization and provide ability to define model-to-model relationships among repository objects, data models and data flows via graphical, attribute level mapping; 7. Extend and share metadata bi-directionally with other tools and through automated synchronization of metadata across multiple instances of the tools; 8. Support multiple secure environments required for SMR and for the MMISR (e.g., development, test, production); and 9. Enable role-based security, security to the attribute level of the database, audit trails and safe storage and handling of data in accordance with all applicable security requirements.
MDM 1.0.0	SI SOW Requirements Definition – MDM Description The contractor shall coordinate with HHS stakeholders to document requirements for master data management to support the collection of data from multiple sources, performing matching, linking and de-duplication and create the following enterprise data services that can be shared throughout the state government and beyond. 1. Master Client Data – integrate client data from disparate systems including Federal verification and commercial data sources and link them to create a master demographic record, containing the most current data from all matched systems, for each citizen receiving State services and creating a unique identifier for each individual; 2. Master Provider Data – match and integrate source records and identifiers from disparate systems to create a master provider record containing the most current data from all matched systems for each provider participating in the HSD programs and those of partner

MMISR R1.0.0 Module Release	Scope
	agencies, create a unique identifier for each provider and maintain relationships between providers, groups and practice locations; 3. Master HSD Data – match and integrate source records and identifiers from disparate systems to create an master agency record to reliably indicate which HHS 2020 participating agency provided, requested or received data from MMISR, with each participating agency to have a unique identifier; 4. Master Employer Data – match and integrate source records and identifiers from disparate systems to create a master employer record containing the most current data from all matched systems for each employer and create a unique identifier for employer. (There is a possibility that this will be handled through an agreement with NM Department of Workforce Solutions.); and 5. Other Master Data as required by individual modules (master claims index, master prior authorization, etc.) General areas of requirements include, as described in the RFP, but at not limited to: 1. Provide a sophisticated matching function to match, link and integrate records, to prevent creation of duplicate records, to provide a configurable method for resolving near matches (controlling the percentage of false positives and false negatives) and to allow the State to manually or automatically link or unlink an entity within an identified index; 2. Improve data quality by identifying and correcting data inconsistencies between systems and data duplication within systems; 3. Support ongoing control of data through established data governance practices that store and maintain items in a consistent fashion and format across all systems; and Enable sharing of data throughout State government by storing essential shared information in each MDMs respective repository.
CCM 1.0.0	SI SOW Requirements Definition – CCM Description The contractor shall coordinate with HHS stakeholders to document requirements for integration of the CCM application into the SI framework. The contractor shall reuse HHS 2020's HSD HP's Notice Generation tool for CCM. The contractor shall develop requirements for encapsulating the CCM tool into the SOA framework to send notices, alerts, forms and other communications by various channels (physical mail, email, text, other) to external consumers, providers, payers, as well as internal Stakeholders. The contractor shall develop requirements for end user access to the CCM applications.

MMISR R1.0.0 Module Release	Scope
ASVV 1.0.0	SI SOW Requirements Definition – Address Standardization Description The contractor shall coordinate with HHS stakeholders to document requirements for a single service used by any HHS 2020 application to standardize and normalize addresses, whether for businesses, consumers, households, or other locations. The Contractor shall reuse SAP Data Services product support address standardization integrate it into the Integration Platform business workflow where it will be used on an as needed basis. The service will also be exposed to any HHS 2020 application as an on demand service as part of the suite of utility services. The contractor shall document requirements for encapsulating address standardization into the SI integration platform. The contractor will provide requirements for configuring the service orchestration framework to incorporate SAP Data Services product into the business workflow.
EDM 1.0.0	SI SOW Requirements Definition – EDM Description The contractor shall coordinate with HHS stakeholders to document requirements for integration of EDM into the SI framework. The contractor shall reuse HSD's EDM tool. The contractor shall develop requirements for encapsulating the EDM tool into the SOA framework to meet the current and future needs of the HHS 2020 Enterprise. The contractor shall develop requirements for end user access to the EDM application.
IDAM 1.0.0	SI SOW Requirements Definition – Security (IDAM) Description The contractor shall coordinate with HHS stakeholders to document requirements for the SI core and each module's integration points 1. Data access and transmission 2. Interfaces 3. Role based access 4. Data security at rest 5. Data encryption Contractor will go through joint application requirements sessions with State and other identified stakeholders to finalize requirements for the SI Platform's security modules which includes Identity and Access Management and Splunk (SIEM), identity proofing, system integrity and system cyber fraud prevention, and Single sign-on as identified in the RFP Section 2.1. Contractor will document the finalized requirements for the SI Platform's security modules through the processes/mechanisms as identified in the RFP Section 2.1.2.4. Contractor will incorporate CMS Standards and Conditions and SOA best practices for requirements. Contractor will compile a Requirements Document for Security.
ASPEN 1.0.0	SI SOW Requirements Definition – ASPEN Description

MMISR R1.0.0 Module Release	Scope
	The contractor shall coordinate with HHS stakeholders to document requirements for a single service used by any HHS 2020 application to integrate with the Legacy ASPEN system. The contractor shall document requirements for integrating ASPEN into the SI integration platform.
CSES 1.0.0	SI SOW Requirements Definition – CSES Description The contractor shall coordinate with HHS stakeholders to document requirements for a single service used by any HHS 2020 application to integrate with the Legacy CSES system. The contractor shall document requirements for integrating CSES into the SI integration platform.
DOH 1.0.0	SI SOW Requirements Definition – DOH Description The contractor shall coordinate with HHS stakeholders to document requirements for a single service used by any HHS 2020 application to integrate with the Legacy DOH system. The contractor shall document requirements for integrating DOH into the SI integration platform.
DS 1.0.0	SI SOW Requirements Definition – Data Services Integration Description Contractor will conduct formal design reviews of the Data Services module's services which will interface via the SI Platform with other modules within HHS 2020. The design reviews will be conducted only for the Integration and not the entire module. Contractor will publish review guidelines prior to scheduling design reviews. Contractor will designate roles and inform participants before design review meetings of their roles and expected contributions. Contractor will schedule design review meetings and invite all required and optional participants. Contractor will gather, organize and publish design materials prior to design review meetings. Contractor will publish meeting goals and agenda items prior to the design reviews. Contractor will inform the Architecture Review Board (ARB) of the design reviews. Contractor will publish results of the design reviews to the ARB. Contractor will ensure all service designs are compliant with the Integration Requirements for Data Services. Contractor will review and vet the quality and completeness of the designs of all services and messages produced to integration with other HHS 2020 assets. Contractor will produce defect reports for design defects. Contractor will formally inform the Data Services vendor of any design changes, and copy the ARB in these communications.
QA 1.0.0	SI SOW Requirements Definition – Quality Assurance Integration Description The Contractor will collaborate with State and Quality Assurance vendor to document requirements for integration of the Quality Assurance module into the HHS 2020 ecosystem that are consistent with the SOA design choices of the Contractor and the State's design criteria of the SI Platform. Such Integration Requirements will include requirements for using the System Migration Repository (SMR) for initial loads of data in the Quality Assurance module, as well as requirements for incremental loads if necessary to support incremental releases of

MMISR R1.0.0 Module Release	Scope
	functionality (or other reason). Integration Requirements will enforce the model where the Quality Assurance module will be populated on a daily basis by subscribing to transactions produced by other modules in HHS 2020, and not through batch updates. Integration Requirements will be used as the primary basis for design of modules by the Quality Assurance vendor. Integration Requirements will be the basis for testing of those modules by the Quality Assurance vendor and the Contractor for integration and performance testing. Integration Requirements will specify design of the message and integration patterns mutually agreed between State and the Contractor such as synchronous messages, “fire and forget,” pub-sub models, splitter/aggregator, content-based routing and other patterns. Integration Requirements will enforce service designs (protocols used, description of services, naming conventions used, standards for asynchronous versus synchronous invocations, message encoding/markup, exception management) that are consistent with other module implementations as well as standards of the SI Platform. Integration Requirements will specify the service and message granularity enforced for other modules and shared schemas. Integration Requirements will specify the use of standard, reusable message schemas enforced by the SI Platform and the Contractor. Integration Requirements will specify that the conversion to/from private representations of data stored by/in the Quality Assurance module to shared schemas will be the responsibility of the Quality Assurance vendor. Integration Requirements will enforce patterns for message and data content security (encryption of data in messages, or entire messages), common to the SI Platform and approved upon integration standards in HHS 2020.
BMS 1.0.0	SI SOW Requirements Definition – BMS Integration Description The Contractor will collaborate with State and the BMS vendor to document requirements for integration of the BMS modules into the HHS 2020 ecosystem that are consistent with the SOA design choices of the Contractor and the State’s design criteria of the SI Platform. Such Integration Requirements will include requirements for using the System Migration Repository (SMR) for initial load of data in the BMS module, as well as requirements for incremental loads if necessary to support incremental releases of functionality (or other reason). Integration Requirements will enforce the model where the BMS module will be populated on a daily basis by subscribing to transactions produced by other modules in HHS 2020, and not through batch updates. Integration Requirements will be used as the primary basis for design of modules by the BMS vendor. Integration Requirements will be the basis for testing of those modules by the BMS vendor and the Contractor for integration and performance testing. Integration Requirements will specify design of the message and integration patterns mutually agreed between State and the Contractor such as synchronous messages, “fire and forget,” pub-sub models, splitter/aggregator, content-based routing and other patterns. Integration Requirements will enforce service designs (protocols used, description of services, naming conventions used, standards for asynchronous versus synchronous

MMISR R1.0.0 Module Release	Scope
	invocations, message encoding/markup, exception management) that are consistent with other module implementations as well as standards of the SI Platform. Integration Requirements will specify the service and message granularity enforced for other modules and shared schemas. Integration Requirements will specify the use of standard, reusable message schemas enforced by the SI Platform and the Contractor. Integration Requirements will specify that the conversion to/from private representations of data stored by/in the BMS module to shared schemas will be the responsibility of the BMS vendors. Integration Requirements will enforce patterns for message and data content security (encryption of data in messages, or entire messages), common to the SI Platform and approved upon integration standards in HHS 2020.
FS 1.0.0	SI SOW Requirements Definition – Financial Services Integration Description The Contractor will collaborate with State and Financial Services vendor to document requirements for integration of the Financial Services module into the HHS 2020 ecosystem that are consistent with the SOA design choices of the Contractor and the State’s design criteria of the SI Platform. Such Integration Requirements will include requirements for using the System Migration Repository (SMR) for initial loads of data in the Financial Services module, as well as requirements for incremental loads if necessary to support incremental releases of functionality (or other reason). Integration Requirements will enforce the model where the Financial Services module will be populated on a daily basis by subscribing to transactions produced by other modules in HHS 2020, and not through batch updates. Integration Requirements will be used as the primary basis for design of modules by the Financial Services vendor. Integration Requirements will be the basis for testing of those modules by the Financial Services vendor and the Contractor for integration and performance testing. Integration Requirements will specify design of the message and integration patterns mutually agreed between State and the Contractor such as synchronous messages, “fire and forget,” pub-sub models, splitter/aggregator, content-based routing and other patterns. Integration Requirements will enforce service designs (protocols used, description of services, naming conventions used, standards for asynchronous vs synchronous invocations, message encoding/markup, exception management) that are consistent with other module implementations as well as standards of the SI Platform. Integration Requirements will specify the service and message granularity enforced for other modules and shared schemas. Integration Requirements will specify the use of standard, reusable message schemas enforced by the SI Platform and the Contractor. Integration Requirements will specify that the conversion to/from private representations of data stored by/in the Financial Services module to shared schemas will be the responsibility of the Financial Services vendor. Integration Requirements will enforce patterns for message and data content security (encryption of data in messages, or entire messages), common to the SI Platform and approved upon integration standards in HHS 2020.

MMISR R1.0.0 Module Release	Scope
UPI 1.0.0	SI SOW Requirements Definition – UPI Integration Description The Contractor will collaborate with the State and the UPI vendor to document requirements for integration of the UPI module into the HHS 2020 ecosystem that are consistent with the SOA design choices of the Contractor and the State’s design criteria of the SI Platform. Such Integration Requirements will include requirements for using the System Migration Repository (SMR) for initial loads of data in the UPI modules as well as requirements for incremental loads if necessary to support incremental releases of functionality (or other reason). Integration Requirements will enforce the model where the UPI module will be populated on a daily basis by subscribing to transactions produced by other modules in HHS 2020, and not through batch updates. Integration Requirements will be used as the primary basis for design of modules by the UPI vendor. Integration Requirements will be the basis for testing of those modules by the UPI vendor and the Contractor for integration and performance testing. Integration Requirements will specify design of the message and integration patterns mutually agreed between State and the Contractor such as synchronous messages, “fire and forget,” pub-sub models, splitter/aggregator, content-based routing and other patterns. Integration Requirements will enforce service designs (protocols used, description of services, naming conventions used, standards for asynchronous versus synchronous invocations, message encoding/markup, exception management) that are consistent with other module implementations as well as standards of the SI Platform. Integration Requirements will specify the service and message granularity enforced for other modules and shared schemas. Integration Requirements will specify the use of standard, reusable message schemas enforced by the SI Platform and the Contractor. Integration Requirements will specify that the conversion to/from private representations of data stored by/in the UPI module to shared schemas will be the responsibility of the BMS and UPI vendors. Integration Requirements will enforce patterns for message and data content security (encryption of data in messages, or entire messages), common to the SI Platform and approved upon integration standards in HHS 2020.
INT 1.0.0	SI SOW Interface Management Plan Description The contractor shall provide an interface management plan that details methodologies to on board trading partners and service providers to the MES. The plan shall include: a. Integration approach/patterns 1) Web services 2) Batch 3) ETL b. Security and access management c. Secure file transfer standards d. Batch processing/job scheduling approach

MMISR R1.0.0 Module Release	Scope
	e. Source and target definitions f. Transformation/ETL strategy g. Validation/Error management approach h. Testing strategy i. Change management The contractor shall use standard out of the box connectors and adaptors to implement interfaces to the MES. If a custom interface is required the contractor shall review the design with HHS prior to implementing the interface. SI SOW Interface Management Activities Description Contractor will, as directed by HSD, conduct and be accountable for the successful outcomes of ongoing interface deployment activities in accordance with the Interface Management Plan. For each interface the contractor will: a. Configure and execute the integration pattern b. Establish access rights and registration for MES, the source system and consumers c. Configure, execute and Manage Secure File Transfer as required d. Define and configure batch processing jobs as required e. Configure ETL/transformation of data as required f. Perform systems integration testing g. Establish performance monitoring and error management processes The Contractor will report Status and Progress related to these areas in the monthly status report.
SO 1.0.0	SI SOW Orchestration Management Plan Description Contractor will develop an Orchestration Management Plan that demonstrates how it will proficiently manage the complex and dynamic work effort to create and maintain the orchestration, business workflows, transactions and messages required to fully implement the business process interactions within the MMISR. The SI vendor will oversee and advise on module vendor's implementation of corresponding orchestration, workflows and message exchanges. The Orchestration Management Plan will include the following categories of information: 1. Development of requirements for utilizing the modules of the SI Platform for implementing the business process interactions between technology solutions, software solutions, network solutions and module functionality. 2. Development of standards for defining and designing orchestration steps and modules of business processing. 3. Development of a services catalog of orchestration repeatable or reusable definitions, designs, steps and processes.

MMISR R1.0.0 Module Release	Scope
	4. The contractor's approach, in combination with the HSD PMO, to leading, implementing, and conducting the processes described in this plan. 5. How the contractor's monthly status report will account for the contractor's execution and progress of contractor roles and duties under this plan. 6. The contractor's role in maintaining and updating this plan. The Contractor will maintain and update the Orchestration Management Plan throughout the contract lifecycle, obtaining HSD approval for modifications to the plan. SI SOW Orchestration Management Services Description Contractor will, in coordination with the HSD PMO, conduct and be accountable for the successful outcomes in implementing and maintaining orchestration of all components of the MMISR solution to accomplish the required interactions between MMISR technical and business processes. This ongoing and continuous work effort will be conducted in accordance with the Orchestration Management Plan. The Contractor will report Status and Progress related to these areas in the monthly status report.

The scope of post-big-bang MMISR module releases will be determined during the planning phases for those releases.

2.8 Release Schedule

This section describes the planning, implementation, and O&M phase dates for the initial big-bang MMISR R1.0.0 and its release modules. The MMISR IMS provides more detailed release schedule information (for example, tasks, resources and dependencies). The MMISR IMS can be found here in SharePoint:

<https://nmhsd.sharepoint.com/:u:/s/H20/Collaboration/SIVD/Eea78gv1T5hLhakVuYpm7wQBnInPHU9yfC50EHt8mQ2WsA>

Table 30: MMISR R1.0.0 Module Release Dates¹

MMISR/ Module Release	CCB ²	RBR ²	IRR	ORR	PRR	PIR ³
ESB/IP 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
SMR 0.1.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD

MMISR/ Module Release	CCB ²	RBR ²	IRR	ORR	PRR	PIR ³
SMR 0.2.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
MDM 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
CCM 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
ASVV 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
EDM 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
IDAM 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
ASPEN 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
CSES 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
DOH 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
DS 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
QA 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
BMS 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
FS 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
UPI 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
INT 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD
SO 1.0.0	N/A	N/A	4/20/2020	8/28/2020	3/1/2021	TBD

1. Dates are subject to change.
2. Since the scope and schedule for MMISR 1.0.0 has already been determined, the planning phase, which includes the CCB and RBR, will not be executed for MMISR 1.0.0.
3. The MMISR 1.0.0 PIR needs to be scheduled for no later than 9/1/2021, six months after MMISR 1.0.0 goes live in the production environment.

The IMS also includes tasks for the delivery of three post-big-bang MMISR patch releases but excludes the delivery of any post big-bang MMSR major or minor releases.

2.9 Release Notifications

MMISR release notifications are used to notify stakeholders and groups of the scope and go-live date for a new release before and after the release goes live in the production environment. MMISR release notifications include:

- A description of release scope (such as new, modified, and retired features) organized by MMISR module.
- Release production go-live date and time
- Release scope not originally scoped for the release but included in the release where applicable

- Release scope originally scoped for the release but not contained in the release where applicable

2.9.1 Release Pre-Go-Live Notifications

The SI Contractor, in collaboration with the module contractors, State-led PMO and NM HSD business owner, will prepare and email a release pre-go-live notification to a to be determined distribution list of MMISR stakeholders and/or groups two days prior to the release's production go live date. The table below represents a sample release pre-go-live notification. A draft version of the Release Notes will be included as an attachment to the notification. Release Notes will focus on explaining the release's user interface related features. See Appendix E for sample NM HSD Release Notes which will be used as a guide for preparing MMISR Release Notes.

Table 31: Sample MMISR Release Pre-Go-Live Notification

On Sunday, January 3, 2021 @5:00PM MT, MMISR 1.1.0 will go live in the production environment. MMISR 1.1.0 delivers the new features and/or improvements listed below by module and described in detail in the attached draft version of the MMISR 1.1.0 Release Notes.		
MMISR 1.1.0 Module Release	PCR #	Feature/Improvement Description
MDM 1.1.0	35746	Master Employer Data – match and integrate source records and identifiers from disparate systems to create a master employer record containing the most current data from all matched systems for each employer and create a unique identifier for employer.
ESB 1.1.0	35733	Provide structured exception and error handling
As a reminder, all MMISR R1.0.0 production issues should be reported to the MMISR Help Desk. Their contact information is as follows: Phone: <<TBD>> Email: <<TBD>> Thank you, The NM HSD MMISR Team		

2.9.2 Release Go-Live Notifications

The SI Contractor, in collaboration with the module contractors, State-led PMO and NM HSD business owner, will prepare and email a release go-live notification to a to-be-determined distribution list of MMISR stakeholders and groups after a successful release production readiness review. The table below represents a sample release go-live notification. A final version of the Release Notes will be included as an attachment to the notification. Release Notes will focus on explaining the release's user interface related features. See Appendix E for sample NM HSD Release Notes, which will be used as a guide for preparing MMISR Release Notes.

Table 32: Sample MMISR Release Go-Live Notification

On Sunday, January 3, 2021 @2:00PM MT, MMISR 1.1.0 went live in the production environment. MMISR 1.1.0 delivers the new features and/or improvements listed below by module and described in detail in the attached MMISR 1.1.0 Release Notes.		
MMISR 1.1.0 Module Release	PCR #	Features/Improvements Description
MDM 1.1.0	35746	Master Employer Data – match and integrate source records and identifiers from disparate systems to create a master employer record containing the most current data from all matched systems for each employer and create a unique identifier for employer.
ESB 1.1.0	35733	Provide structured exception and error handling
As a reminder, all MMISR R1.0.0 production issues must be reported to the MMISR Help Desk. Their contact information is as follows: Phone: <<TBD>> Email: <<TBD>> Thank you, The NM HSD MMISR Team		

2.9.3 Actors

The following table lists the actors, along with their roles and responsibilities, for the release notifications process.

Table 33: Release Notification Process Actors

Actor	Roles and Responsibilities
SI Contractor	- Email release pre-go-live and go-live notifications to a to-be-determined distribution list of MMISR stakeholders and groups. - Prepare release pre-go-live and go-live notifications.
Module Contractors	Prepare release pre-go-live and go-live notifications.
State-led PMO	Prepare release pre-go-live and go-live notifications.

See the MMISR Communications Management Plan for a detailed description of release notifications.

2.10 Release Strategy Process Improvement

Process improvement is the proactive task of identifying, analyzing, and improving existing processes within an organization to optimize them and to meet new quotas or standards of quality. Process

improvements and lessons learned related to a release's project management, system development, and certification will be collected as a part of each release's Post Implementation Review described above.

2.11Release Strategy Training

Staffing acquisition is the process used to find potential new resources, interview and determine if the potential new resource meets the position requirements, make offers of employment, and hire the resources. Each MMISR project participant will document the staffing acquisition processes in their specific Resource Management Plan.

When new resources join the project, enterprise-level on-boarding activities must be completed. These activities include completing enterprise-level MMISR training. Understanding the RSP processes, roles and responsibilities are part of the enterprise-level training curriculum. Enterprise-level training includes Blackboard web training. All resources must complete Blackboard training upon on-boarding. NM HSD will provide access to the Blackboard training site. The appropriate Blackboard training sessions for the resource will be available on the Blackboard website. The resource must complete their assigned Blackboard training and provide the certificate for each training course to NM HSD.

See the Staffing Model and Resource Management Plan for a detailed description of the release strategy training activities which are a part of the MMISR project's staff acquisition process.

3 Medicaid Management Information System Certification

This section describes the Medicaid Management Information System (MMIS) certification approach for ensuring the RSP meets the CMS release strategy requirements.

As identified in Appendix B of the Medicaid Enterprise Certification Toolkit (MECT), the RSP is a component of the technical/SDLC rollout. CMS will review the RSP during the following CMS formal review:

- R2, Operational Milestone Review

CMS may also review this deliverable during informal reviews.

There are no MECT Checklists items attributable to the Release Plan.

4 Applicable Standards

The applicable standards section of the deliverable will identify the standards for all aspects of this deliverable. The following is an initial set of standards the SI Contractor may update over time:

- Project Management Body of Knowledge (PMBOK® 6 Edition)
- CMS eXpedited Life Cycle (XLC) Release Plan Template Version 3.0 dated June 2, 2016

5 Assumptions/Constraints/Risks

This section documents the RSP's assumptions, constraint, and risks.

5.1 Assumptions

This section identifies the statements believed to be true and from which a conclusion was drawn to define the RSP.

- End-user and O&M team training will be conducted using a train-the-trainer approach whereby instructors will be trained to, in turn, train the O&M team and end users

5.2 Constraints

This section identifies any limitations that must be considered during release management.

- The MMISR project does not have a Release Manager.
- The MMISR project does not have a dedicated training environment.

5.3 Risks

All MMISR project risks are maintained in the MMISR project SharePoint Risk Log accessible from the following link: <https://nmhsd.sharepoint.com/sites/H20/Lists/Risks/MMISR.aspx>

6 Requirements Traceability

This section documents requirements satisfied by the deliverable, in the following form:

- Request for Proposal (RFP)
 - Page 141, Section 2.04
 - Page 148, Section 2.44
 - Page 148, Section 2.45
 - Page 155, Section 5.18
- Proposal
 - Page 164, Section 2.2.4
 - Page 195, Section 2.2.44
 - Page 196, Section 2.2.45
 - Page 229, Section 2.5.18
- SOW
 - Section 20, PMO20 – Release Strategy

7 Appendices

7.1 Appendix A: List of Acronyms

The table below contains a list of acronyms used in the RSP. For a comprehensive, project-wide list of acronyms, the reader can consult the Master Acronyms List maintained on the on MMISR project SharePoint site at [Shared Resources on SharePoint](#).

Table 34: List of Acronyms

Acronym	Definition
API	Application Program Interface
ARB	Architecture Review Board
ASPEN	Automated System Program and Eligibility Network
ASVV	Address Standardization, Verification and Validation
BMS	Benefit Management Services
BTC	Business Transformation Council
BVT	Breadth Verification Test
CCB	Change Control Board
CCM	Customer Communications Management

Acronym	Definition
CCMP	Change Control Management Plan
CD	Continuous Deployment
CI	Configuration Item
CMS	Centers for Medicare and Medicaid Services
COTS	Commercial Off-the-Shelf
CSCC	Consolidated Customer Service Center
CSES	Child Support Enforcement System
DED	Deliverable Expectations Document
DGC	Data Governance Council
DoH	Department of Health
DS	Data Services
EDM	Electronic Documentation Management
ESB	Enterprise Service Bus
ESS	Enterprise Shared Service
ETL	Extract Transform and Load
FS	Financial Services
HHS	Health and Human Services
HSD	Human Services Department
IAW	Impact Assessment Worksheet
IdAM	Identity and Access Management
IMS	Integrated Master Schedule
INT	Interfaces
IP	Integration Platform
IRR	Implementation Readiness Review
ITIL	Information Technology Infrastructure Library
ITSM	Information Technology Service Management
KPI	Key Performance Indicator
LMI	Legacy Module Integration
MARS-E	Minimum Acceptable Risk Standards for Exchanges
MDM	Master Data Management
MECT	Medicaid Enterprise Certification Toolkit

Acronym	Definition
MES	
MMIS	Medicaid Management Information System
MMISR	Medicaid Management Information System Replacement
NM	New Mexico
NMI	New Module Integration
O&M	Operations and Maintenance
OC	Omnicaid
PCR	Project Change Request
PIR	Post Implementation Review
PMBOK	Project Management Body of Knowledge
PMO	Project Management Office
PRR	Production Readiness Review
QA	Quality Assurance
QMP	Quality Management Plan
RBP	Release Baseline Plan
RBR	Release Baseline Review
RFP	Request for Proposal
RSP	Release Strategy Plan
SAP	Systems, Applications & Products in Data Processing (a software company)
SDLC	System Development Life Cycle
SI	System Integration
SIEM	Identity and Access Management and Splunk
SLA	Service Level Agreement
SMR	Systems Migration Repository
SO	Service Orchestration
SOA	Service-Oriented Architecture
SOW	Statement of Work
SSO	Single Sign On
SSP	System Security Plan
TBD	To Be Determined

Acronym	Definition
TMP	Test Management Plan
UAT	User Acceptance Testing
UP	Unified Portal
UPI	Unified Public Interface
XLC	eXpedited Life Cycle
XML	Extensible Markup Language

7.2 Appendix B: Glossary

This section will refer the reader to the MMISR project SharePoint site at [Shared Resources on SharePoint](#) for a comprehensive of list of project-specific terminologies.

7.3 Appendix C: MECT Checklist

There are no Medicaid Enterprise Certification Toolkit (MECT) Checklist items attributable to the RSP.

7.4 Appendix D: RBP Template

The Release Baseline Plan template can be found in SharePoint here:

<https://nmhsd.sharepoint.com/sites/H20/Collaboration/SIVD/Shared%20Documents/System%20Integrator/Shared%20Resources/MMISR%20Baseline%20Document%20Template.docx>

7.5 Appendix E: Sample NM HSD Release Notes

The following figures contain NM HSD Yes NM 1.98.0 Release Notes, which will be used as template for preparing MMISR Release Notes.

Figure 12: Operational Testing

YES NM 1.98.0 Release Notes

Release Date	Oct 29, 2018
Issues	14 issues
Status	IN PRODUCTION
Author	Ed Rivera

- Summary
- User Release Notes
- Important highlights from this release
- All updates for this release
 - New Feature
 - Improvements
 - Bugs
 - Tasks

Summary

YES NM release 1.98.0 includes one new feature, three improvements, eight bug fixes and two tasks completed.

User Release Notes

The YES NM 1.98.0 release was a hot deployment on October 29, 2018 starting at 7:30 AM. The YES NM site remained up and running during this release.
YES Admin Portal is always a cold deployment, so YES Admin Portal was down for a few minutes between 7:30 AM and 8:00 AM for this release.

Important highlights from this release

- Changes and bug fixes were applied to RMC/RMB.
- The signature page was modified.
- The PS application was modified.
- Various bugs were fixed addressing validations issues, unexpected errors and data integrity.

All updates for this release

New Feature

- YES-10479 **DONE** When a client has benefits that are up for renewal and the RMB button and RMC buttons are available, a dialogue box will appear if they select the RMC button asking "You have selected to Report a Change. Just a reminder that your benefits are due for renewal, if you want to renew your benefits click here. If you do not want to renew your benefits and just report a change click here." The RMC and RMB buttons will be available below the new text and the applicant may choose either RMC or RMB.




Improvements

- YES-10544 **DONE** Secretary of State address and phone number has been changed in the Review Application/Register To Vote section in YES NM.




- YES-10417 **DONE** Data displayed in YES Admin Portal Case View/YES NM home page is now sorted to match YES NM home page. YES Admin portal is used by workers to help an applicant/recipient navigate the YES NM site by viewing what the account owner views.



- YES-10348 **DONE** PE applications now have a restriction on the date for "What is the anticipated release date?". This date is now limited to ten days into the future.

Bugs

- YES-10553 **DONE** RMC was crashing with an unknown utility type retrieved from ASPEN. The word Unknown is now displayed for unknown utility expenses from ASPEN. There is another task to handle the deprecated data coming from ASPEN.
- YES-10542 **DONE** RMC code was modified to handle frequent use of the back button that could cause navigation issues.
- YES-10536 **DONE** Proper validation was added for the first names and last names for a non-custodial parent in RMC. The names for non-custodial parents are now limited to thirty characters to be consistent with the YES NM website.
- YES-10523 **DONE** The Webmaster Comments report in YES Admin Portal had a bug fixed where it was difficult for the user to change the original choice for the start date parameter.
- YES-10518 **DONE** Change Your Enrollment for MCO switching was modified to handle the possibility of an applicant making an error when not making a selection of individuals to switch.



- YES-10503 **DONE** RMC had a bug where move in individuals were added to the application and later deleted from the application for some reason. The bug was that deleted individuals were unintentionally being sent to ASPEN. Individuals added to the RMC then later deleted are not being sent to ASPEN now.
- YES-10416 **DONE** A bug was fixed where the download for YES Admin Portal/LIHEAP Reports/Vendor Monthly Report was downloading as a .zip file. The report now downloads as the local Excel file version.
- YES-08708 **DONE** A bug was fixed for applicants processing an AFB with LIHEAP and making changes to the original secondary provider for electric. The code now handles the condition where the applicant goes back and makes the choice that they do not have electric.

Tasks

- YES-10543 **DONE** Spanish translations were added for YES-10479 when the RMC and RMB buttons are both available.
- YES-10533 **DONE** A matrix of YES Admin Portal roles was documented for future development.

7.6 Appendix F: Record of Changes

Changes to any part of the RSP after initial approval will follow the accepted change management process documented in the MMISR CCMP and will be recorded in the table below.

Table 35: Record of Changes

Version Number	Date	Author/Owner	Description of Change
v0.1	9/13/2018	Adrian Ball	DED Draft

Version Number	Date	Author/Owner	Description of Change
v0.2	9/23/2018	Adrian Ball	DED Final with comments Addressed HSD comments in the attached.
v0.3	9/26/2018	Adrian Ball	DED Final with comments Addressed HSD feedback received at the 9/25 DED Final Walkthrough Meeting, specifically: a. In Section 1.2 (Purpose), specified that BMC Discovery is TurningPoint's proposed Configuration Management Database tool b. In Section 2.1 (major, minor, and patch release management), added release complexity to the criteria for determining a release type (such as, major, minor, and patch) and noted that each release type could have its own release strategy. c. In Section 2.1.1 (Planning), noted that details regarding the content of the RBP and purpose of the RBR would be described in this section too. d. Removed Sections 2.1.2 (Requirements Analysis), 2.1.3 (Design) and 2.1.4 (Development) e. Update Sections 2.1.6 (Implementation) to align with CMS Testing Framework Overview provided by Wes and renamed the section "Production Implementation." f. Update Sections 2.1.7 (O&M) to align with CMS Testing Framework Overview provided by Wes and renamed the section "Production O&M."
v0.4	10/2/2018	Adrian Ball	DED Final updated to reflect comments received from Paul Price on 10/1, specifically: a. Removed Section 2.1.5 (Testing) b. Rewrote Section 2.1.6 (Production Implementation)
v0.5	11/26/2018	Adrian Ball	Draft

8 Deliverable Format

This deliverable will be submitted as a Microsoft Word document. Its estimated size is 20 pages.

9 Deliverable Acceptance Criteria

The table below lists the deliverable acceptance criteria.

Table 36: Deliverable Acceptance Criteria

Item	Description
1	Deliverable includes all DED sections and information.
2	Deliverable meets requirements in Section 6.
3	Deliverable meets quality checklist, including style guide check list item. Link to checklist: Shared Resources folder on SharePoint

10 Deliverable Schedule

The table below lists the deliverable schedule.

Table 37: Deliverable Schedule

Step	Completion Date	Description	Participants
1	8/31/2018	PMO20 Release Strategy Plan DED Kick Off Mtg	TPGSI, HSD
2	9/13/2018	Post DED-Draft to SharePoint	TPGSI
3	9/17/2018	Conduct DED-Draft Walkthrough	TPGSI, HSD
4	9/19/2018	Provide DED-Draft Feedback	HSD
5	9/24/2018	Conduct DED-Final Joint Review Meeting	TPGSI, HSD
6	10/15/2018	Post Deliverable-Draft to SharePoint	TPGSI
7	10/22/2018	Review Draft Deliverable and Provide Feedback	HSD
8	11/9/2018	Incorporate feedback and Submit Final to HSD	TPGSI
9	11/28/2018	Provide Disposition for Deliverable-Final	HSD
